



Government of Telangana

**Education Department**

TGEWIDC



**YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOL**  
GOVERNMENT OF TELANGANA

 **UR ARCHITECTS**

 **INTEGRATED  
RESIDENTIAL SCHOOLS**  
YOUNG INDIA  
TELANGANA



**YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOL**  
GOVERNMENT OF TELANGANA

**UR ARCHITECTS**





YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOL  
GOVERNMENT OF TELANGANA



GOVERNMENT OF TELANGANA




YOUNG INDIA  
INTEGRATED RESIDENTIAL SCHOOL

## YIIRS Program Status

<b>Program Scope</b>	<b>Sanctioned</b>	<b>Sanction Awaited</b>	<b>Tenders settled</b>	<b>Tenders to be Settled</b>	<b>Works Commenced</b>	<b>Site Issues</b>
<b>105</b>	<b>79</b>	<b>26</b>	<b>76</b>	<b>3</b>	<b>65</b>	<b>28</b>

**Total 105 Schools @ Rs. 200 Cr Each = Rs. 21,000 Cr**

**CASHFLOW REQUIREMENT**

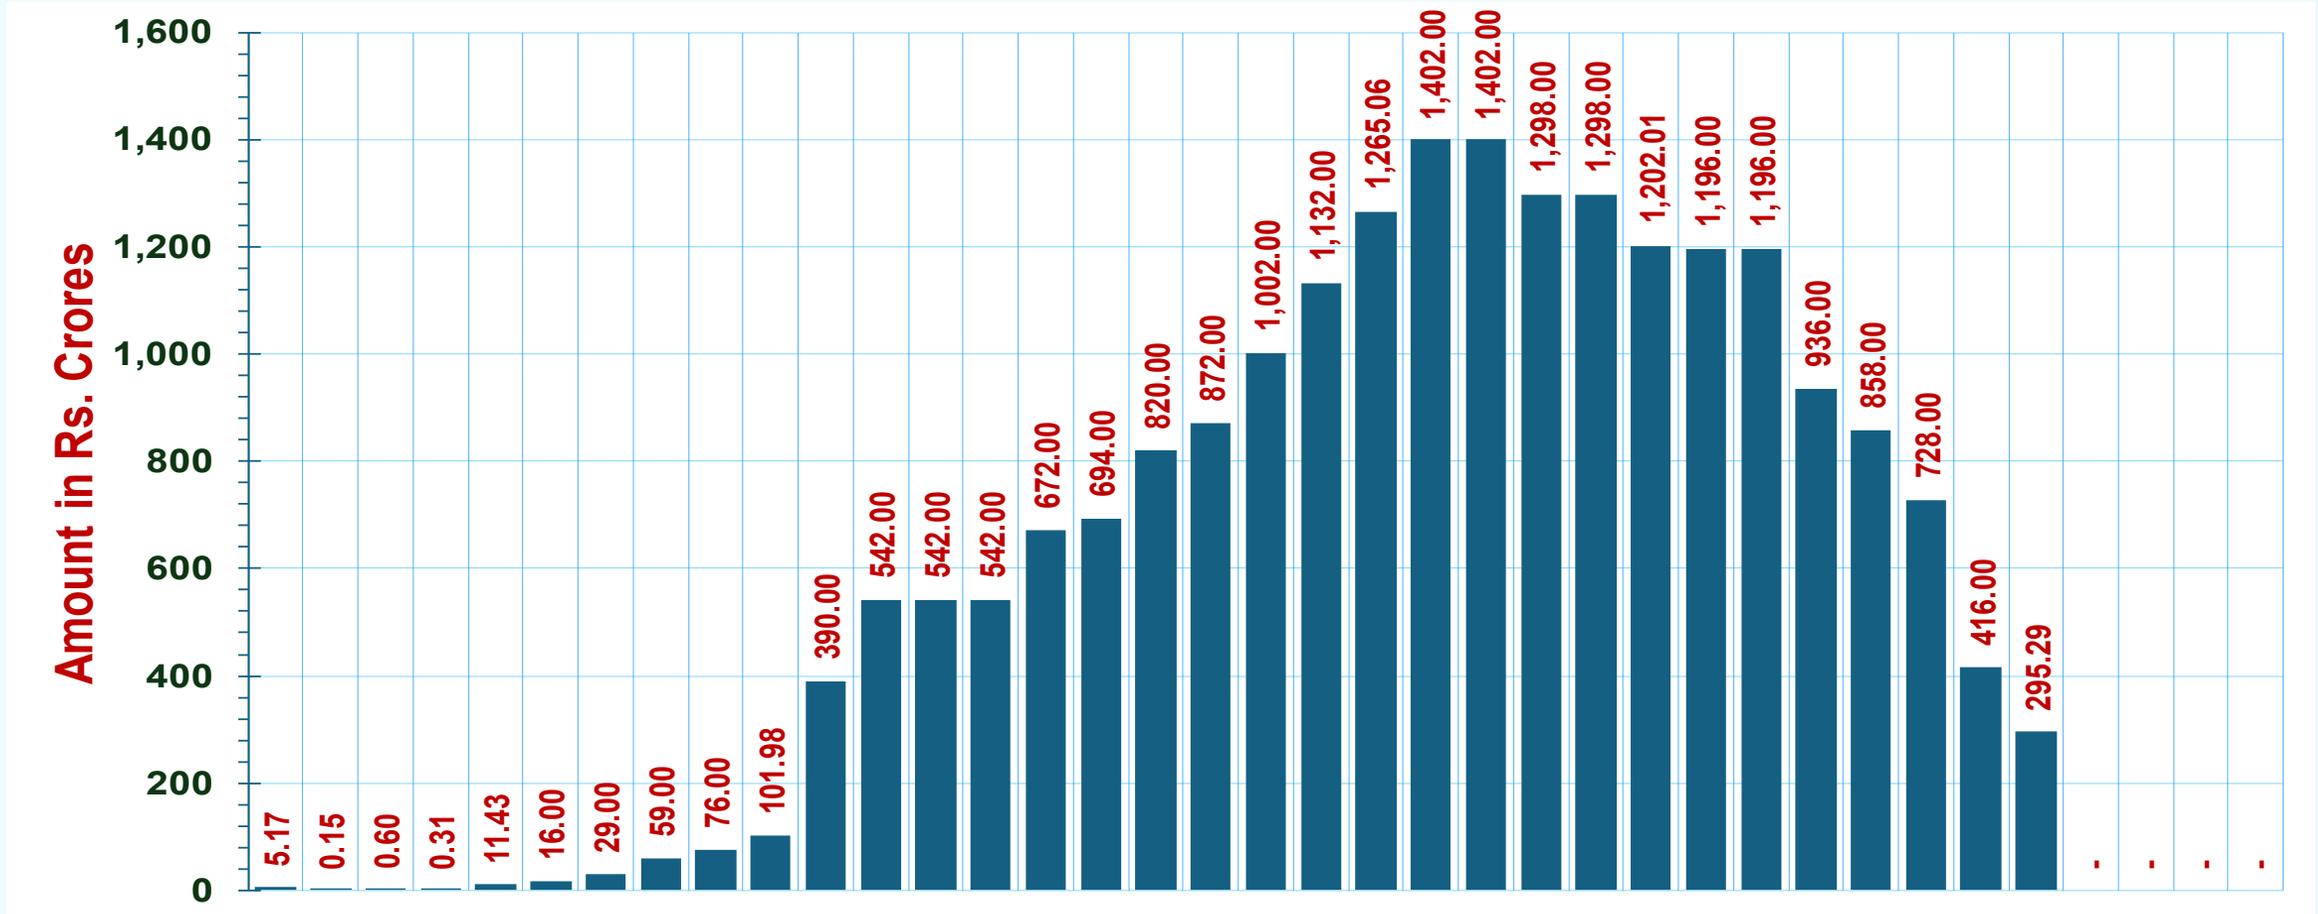

Month	Jun-25	Jul-25	Aug-25	Sep-25	Oct-25	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27	Mar-27	Apr-27	May-27	Jun-27	Jul-27	Aug-27	Sep-27	Oct-27	Nov-27	Dec-27	Jan-28	Feb-28	Mar-28	Apr-28	May-28	Jun-28
Annual Cashflow Requirement	Rs.299.64 Cr in FY : 2025-26										Rs.9875.058 Cr in FY : 2026-27										Rs.10825.30224 Cr in FY : 2026-27																

# MONTHLY CASHFLOW REQUIREMENT

Sl	Month	Cashflow Required in Rs. Cr	Year 2025-26	Year 2026-27	Year 2027-28
1	Jun-25	5.17	5.17		
2	Jul-25	0.15	0.15		
3	Aug-25	0.60	0.60		
4	Sep-25	0.31	0.31		
5	Oct-25	11.43	11.43		
6	Nov-25	16.00	16.00		
7	Dec-25	29.00	29.00		
8	Jan-26	59.00	59.00		
9	Feb-26	76.00	76.00		
10	Mar-26	101.98	101.98		
11	Apr-26	390.00		390.00	
12	May-26	542.00		542.00	
13	Jun-26	542.00		542.00	
14	Jul-26	542.00		542.00	
15	Aug-26	672.00		672.00	
16	Sep-26	694.00		694.00	
17	Oct-26	820.00		820.00	
18	Nov-26	872.00		872.00	
19	Dec-26	1,002.00		1,002.00	
20	Jan-27	1,132.00		1,132.00	
21	Feb-27	1,265.06		1,265.06	
22	Mar-27	1,402.00		1,402.00	
23	Apr-27	1,402.00			1,402.00
24	May-27	1,298.00			1,298.00
25	Jun-27	1,298.00			1,298.00
26	Jul-27	1,202.01			1,202.01
27	Aug-27	1,196.00			1,196.00
28	Sep-27	1,196.00			1,196.00
29	Oct-27	936.00			936.00
30	Nov-27	858.00			858.00
31	Dec-27	728.00			728.00
32	Jan-28	416.00			416.00
33	Feb-28	295.29			295.29
34	Mar-28				
		<b>21,000.00</b>	<b>299.64</b>	<b>9,875.06</b>	<b>10,825.30</b>

## FUNDING SOURCES

- a) State budget under the Secretary, TREIS, ₹500 crore  
₹10 crore released so far. BRO Released for Rs. 250.00 Crores.
- b) DMFT deposits with the District Collectors ₹450 crore  
Released Rs. 28.96 Crores so far
- c) External assistance through loans  
The NABARD loan for an amount of Rs. 288.75 Crores have been sanctioned.

## DETAILS OF EXPENDITURE

- a) Total value of work done as on date: ₹91.5 crores.
- b) Total expenditure incurred as on date: ₹39.83 crores.

## Cost Break-up per One School

Sl	Particulars	Total Cost in Rs. Cr	EA in Rs. Cr	State Budget in Rs. Cr
<b>a1</b>	<b>Cost of Infrastructure for 1 School</b>			
	(Academic Block + Lab)	200.000		
	One academic block of 27,793.08 sft at Rs. 3170 per sft		10.367	189.633
	Cost of Brick & Mortar - Infrastructure - A	200.000	10.367	189.633
<b>b1</b>	<b>Cost of Equipment</b>	14.352	14.352	-
	Technology-Integrated Learning Ecosystems			
<b>b2</b>	<b>Cost of Software</b>	1.128	1.128	-
	Advancing Future-Ready Education			
<b>b3</b>	<b>Training cost - Recurring (2-5) years</b>	12.716	12.716	-
	Hub-school Training for all Teachers			
	Cost of Digital Infrastructure & Training - B	28.196	28.196	-
	<b>Total Project cost per School</b>	229.269	38.563	189.633
		100%	16.90%	83.10%

## Cost Break-up Overall Program

Sl	Particulars	Total Cost in Rs. Cr	EA in Rs. Cr	State Budget in Rs. Cr
<b>a1</b>	<b>Cost of Infrastructure for all 105 School</b> (Academic Block 8 classrooms + 2 Labs)	<b>21,000.000</b>		
	One academic block of 29, 18,273.40 sft at Rs. 3170 per sft		<b>1,088.516</b>	<b>19,911.484</b>
	Cost of Brick & Mortar - Infrastructure - A	<b>21,000.000</b>	<b>1,088.516</b>	<b>19,911.484</b>
<b>b1</b>	<b>Cost of Equipment</b> Technology-Integrated Learning Ecosystems	<b>1,506.960</b>	<b>1,506.960</b>	-
<b>b2</b>	<b>Cost of Software</b> Advancing Future-Ready Education	<b>118.440</b>	<b>118.440</b>	-
<b>b3</b>	<b>Training cost - Recurring (2-5) years</b> Hub-school Training for all Teachers	<b>1,335.191</b>	<b>1,335.191</b>	-
	Cost of Digital Infrastructure & Training - B	<b>2,960.591</b>	<b>2,960.591</b>	-
	<b>Total Program cost for all 105 Schools</b>	<b>23,960.591</b>	<b>4,049.107</b>	<b>19,911.484</b>
		<b>100%</b>	<b>16.90%</b>	<b>83.10%</b>

# YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS

## Facilities proposed in YIIR Schools

- Academic Block –  
5<sup>th</sup> to 12<sup>th</sup> – 64 Classrooms  
at 40 Students per section = 2,560 Students
- Dormitory Accommodation –  
5<sup>th</sup> to 8<sup>th</sup> – Two Tier bed arrangement for 1,280 Students  
9<sup>th</sup> to 12<sup>th</sup> – Single Tier bed arrangement for 1,280 Students
- Dining-cum-Kitchen –  
2 Halls for 1,280 Students in Two shifts
- Staff Accommodation –  
Principal Quarter 1 each – 3 BHK = 4 Quarters  
Teaching Staff Quarters 6 each – 2 BHK = 24 Quarters  
Maintenance staff 2 each – 1 BHK = 8 Quarters  
Wardens (Teaching) In Dormitory = 26 Studio Apartments  
**Total Accommodation = 62 Staff**


# YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS

## Built-up Area proposed in YIIR Schools

Sl.	Name of the block	Units	Blocks	Floors	Total Built-up area in sq. ft
1	ACADEMIC BLOCK		4	G+2	1,60,339
2	DORMITORY BLOCK		6	G+3	2,57,451
3	DINING CUM KITCHEN BLOCK		1	G+1	41,860
4	3 BHK PRINCIPAL QUARTERS	4	1	G+1	7,483
5	2 BHK STAFF QUARTERS	24	1	G+3	61,738
6	1 BHK QUARTER	8	1	G+1	7,324
				Total	5,36,194

# STATUS OF YIIRS-KODANGAL

<b>Village</b>	Polepally and Hakimpet
<b>Mandal</b>	Dudyala
<b>District</b>	Vikarabad
<b>Survey No</b>	67 of Polepally, Sy. No. 243, 244, 245, 247, 252 of Hakeempet
<b>Land Extent</b>	Ac 20.0
<b>Contractor</b>	M/s. KLSR Infratech Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm

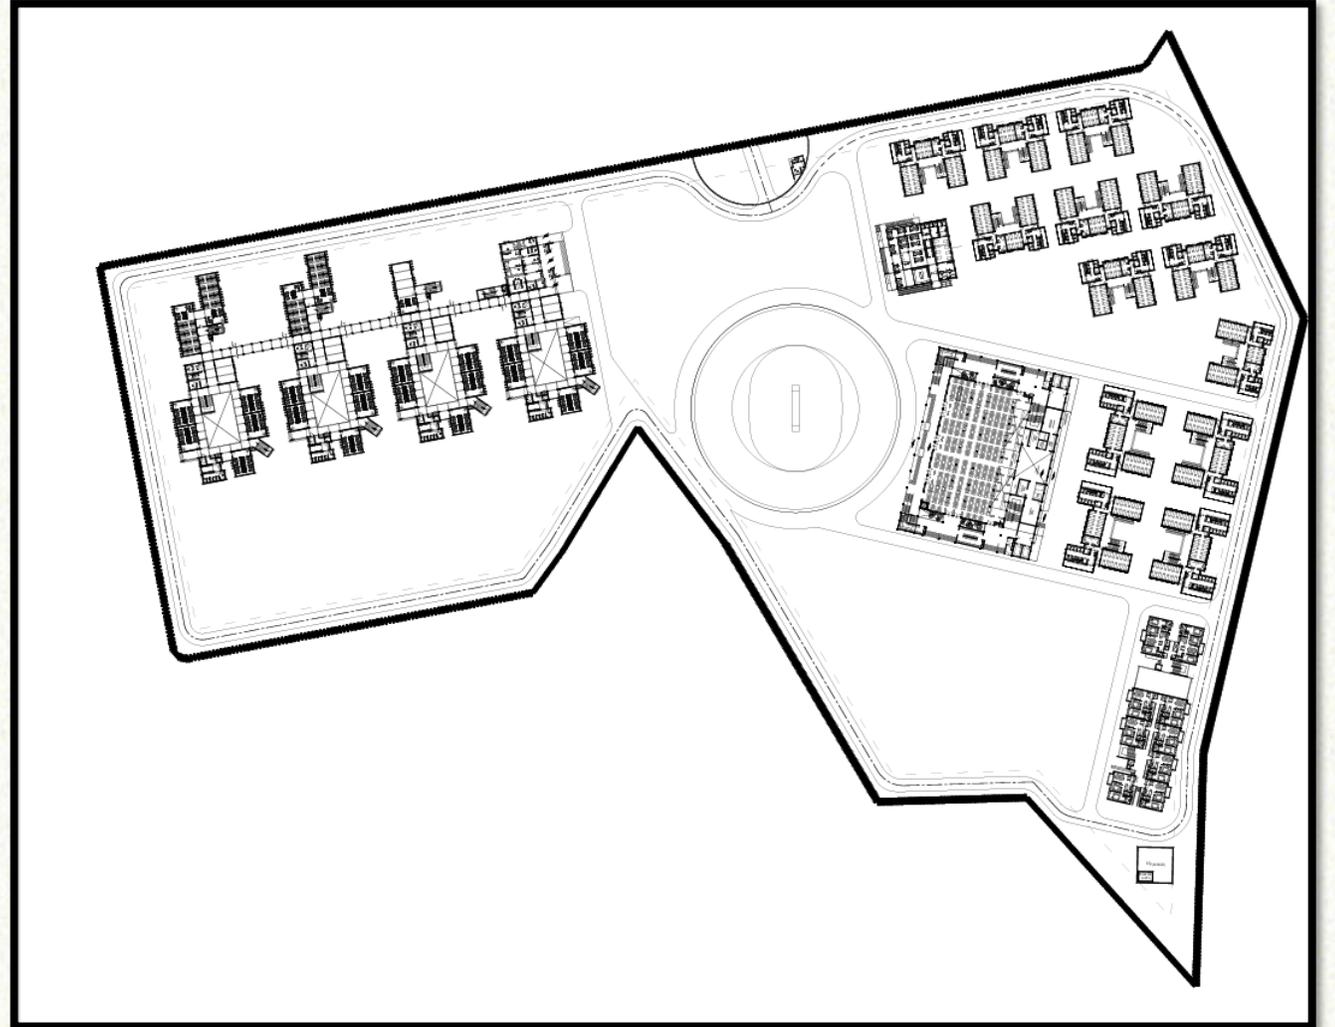

# STATUS OF YIIRS-MADHIRA

<b>Village</b>	Laxmipuram
<b>Mandal</b>	Bonakal
<b>District</b>	Khammam
<b>Survey No</b>	401/1, 401/20, 401/21, 401/22, 401/23 & 401/24
<b>Land Extent</b>	Ac 23.30
<b>Contractor</b>	M/s. BPR Infrastructure Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-MADHIRA

- The work is completed up to Roof Beam in Academic Building and Junior Hostel.
- Mivan Shuttering work is in progress for Academic Building and Junior Hostel.

### ACADEMIC BLOCK




### JUNIOR HOSTEL BLOCK



# STATUS OF YIIRS-HUZURNAGAR

<b>Village</b>	Gaddipally
<b>Mandal</b>	Garidepally
<b>District</b>	Suryapet
<b>Survey No</b>	57
<b>Land Extent</b>	Ac 20.0
<b>Contractor</b>	M/s. KLSR Infratech Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm

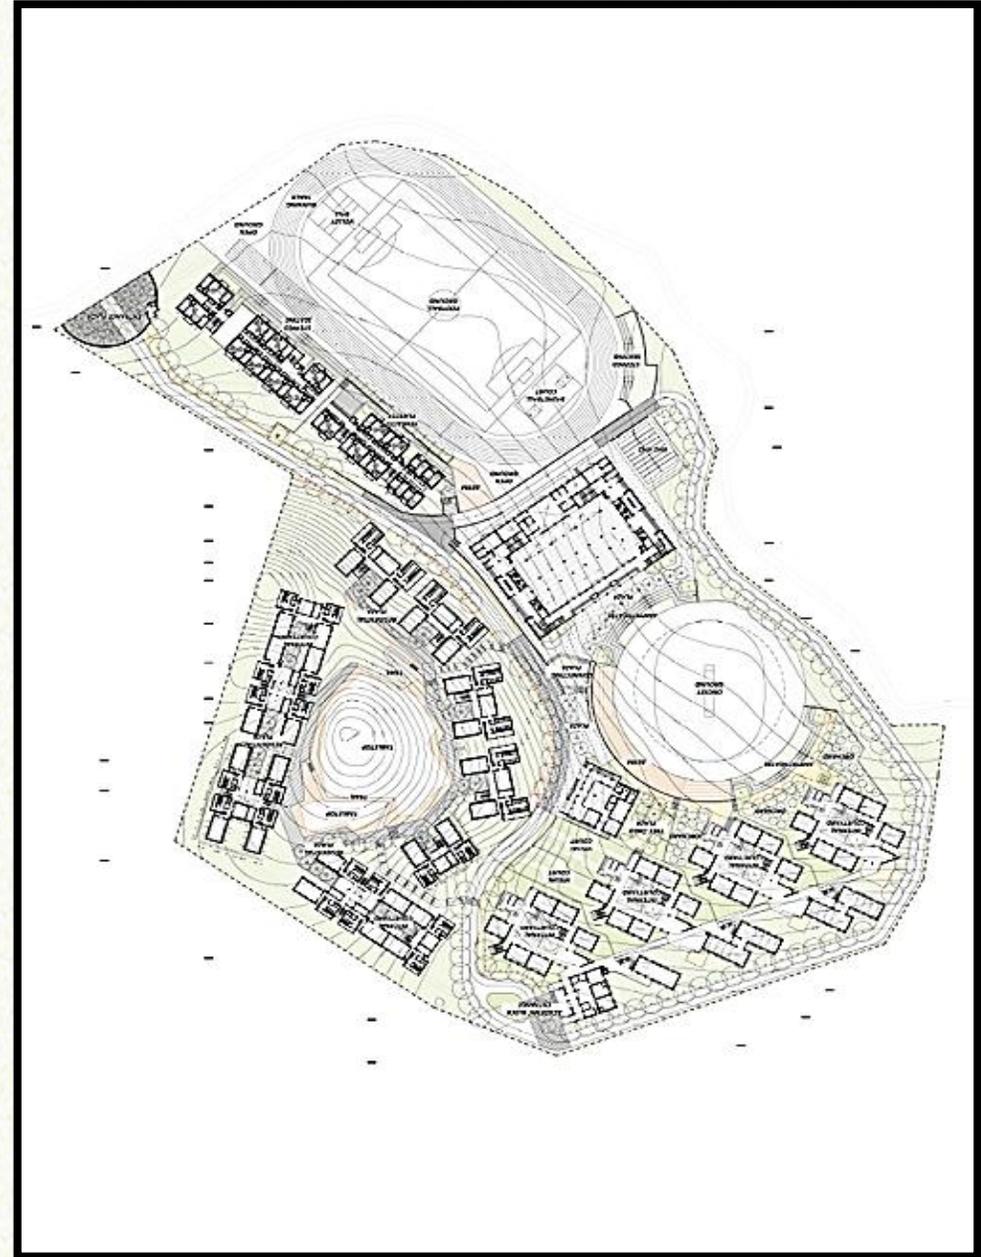

## STATUS OF YIIRS-HUZURNAGAR

- Earth work excavation is in progress in Junior Hostels & Academic Building.

### ACADEMIC BLOCK



### Junior Hostels



# STATUS OF YIIRS-MANTHANI

<b>Village</b>	Adavi Somanpalli
<b>Mandal</b>	Manthani
<b>District</b>	Peddapalli
<b>Survey No</b>	192
<b>Land Extent</b>	Ac 25.60
<b>Contractor</b>	M/s. Siddartha Constructions
<b>Consultant</b>	Architecture Paradigm

1. MAIN ENTRY
2. ADMIN
3. ACADEMIC BLOCK
4. SENIOR HOSTEL
5. JUNIOR HOSTEL
6. CLASS IV WORKERS UNIT
7. STAFF - 2BHK
8. STAFF - 3BHK CLUSTER
9. MULTIPURPOSE HALL
10. DINING BLOCK
11. PARENTS LOUNGE
12. CRICKET FIELD
13. FOOTBALL FIELD
14. VOLLEYBALL COURT
15. BASKETBALL COURT
16. KHO KHO COURT
17. KABADDI COURT
18. SECURITY CABIN
19. STP
20. UGR TANKS WITH PUMP ROOMS
21. ELECTRICAL YARD



## STATUS OF YIIRS-MANTHANI

- Earth work excavation for Academic Building is in progress



# STATUS OF YIIRS-HUSNABAD

<b>Village</b>	Thangellapally
<b>Mandal</b>	Koheda
<b>District</b>	Siddipet
<b>Survey No</b>	Sy. No. 742, 764
<b>Land Extent</b>	Ac 17.0
<b>Contractor</b>	M/s. BPR Infrastructure Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-HUSNABAD

- The Plinth Beam for the Academic Building is in progress.
- The Foundations for the Junior Hostels Building is in progress.

### ACADEMIC BUILDING



### JUNIOR HOSTEL



# STATUS OF YIIRS-ANDOLE

**Village** Baswapur  
**Mandal** Pulkal  
**District** Sangareddy  
**Survey No** 417  
**Land Extent** Ac 31.02  
**Contractor** M/s. Sai Pavani Constructions  
 Ind P Ltd  
**Consultant** M/s. Architecture Paradigm  
**Site Issues** Irrigation NOC is required.



## STATUS OF YIIRS-ANDOLE


- Foundations for Academic Building is in progress.

### ACADEMIC BLOCK



# STATUS OF YIIRS-VIKARABAD

<b>Village</b>	Alampally
<b>Mandal</b>	Vikarabad
<b>District</b>	Vikarabad
<b>Survey No</b>	Bila Dhakila
<b>Land Extent</b>	Ac 20.0
<b>Contractor</b>	M/s. KLSR Infratech Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm
<b>Site Issues</b>	Proposal is with the CCLA.

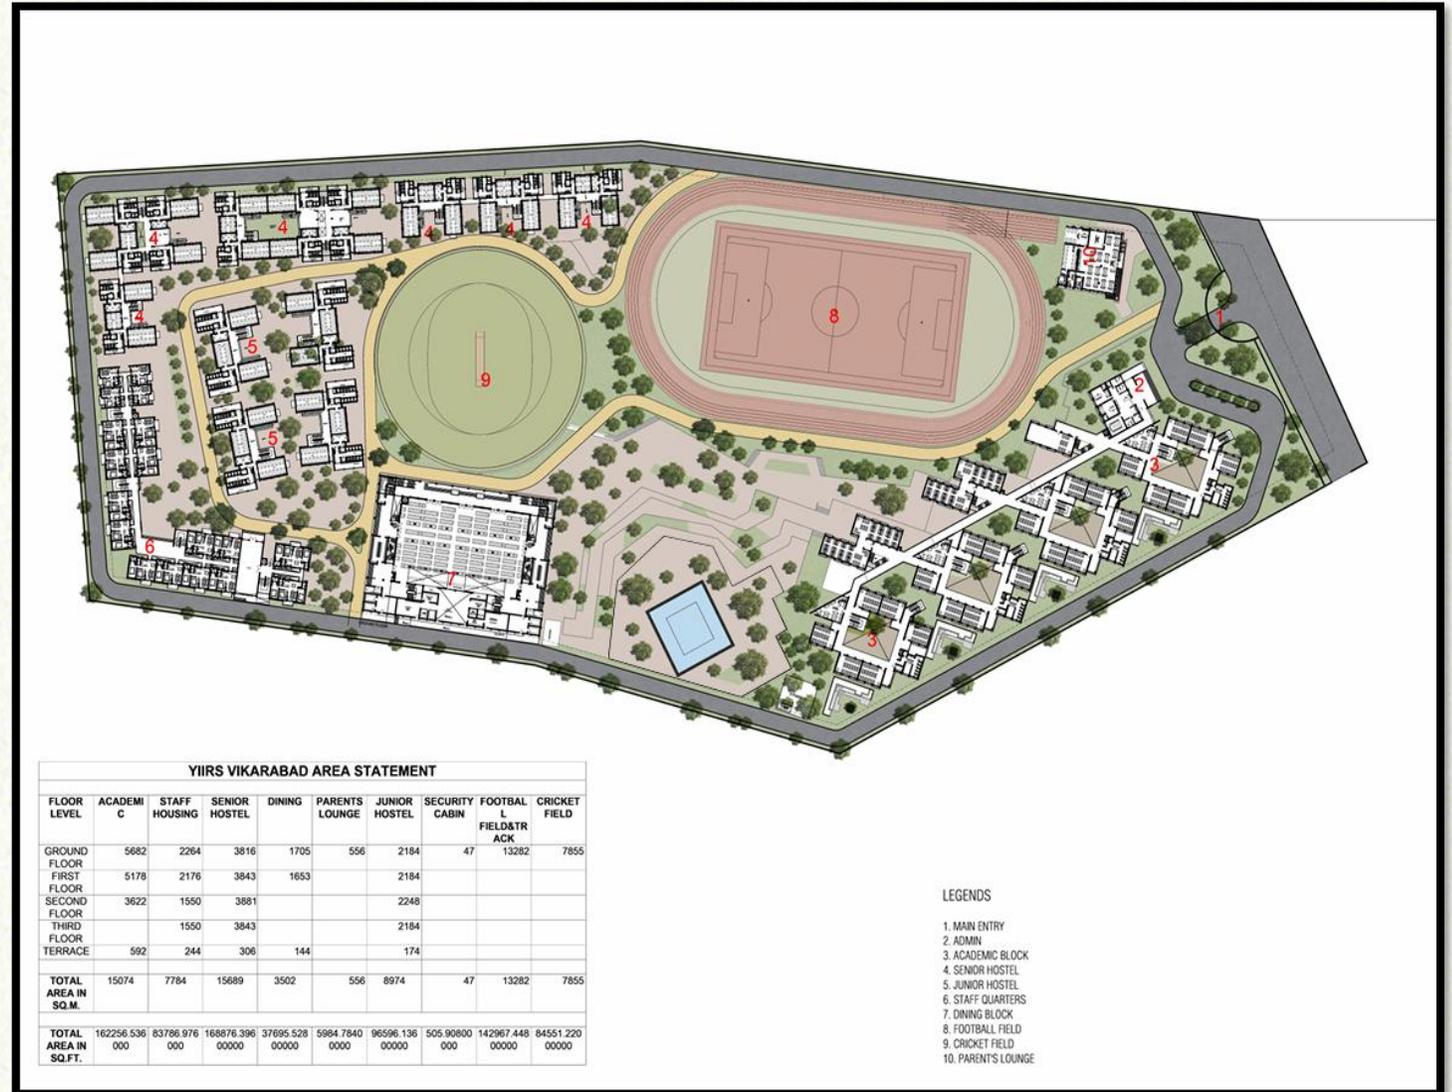


## STATUS OF YIRS-VIKARABAD

- Earthwork excavation for Academic Building is in progress



# STATUS OF YIIRS-SHADNAGAR

**Village** Kondurg (West)  
**Mandal** Kondurg  
**District** Rangareddy  
**Survey No** 109  
**Land Extent** Ac 20.0  
**Contractor** M/s. KMV Projects Ltd  
**Consultant** M/s. Architecture Paradigm

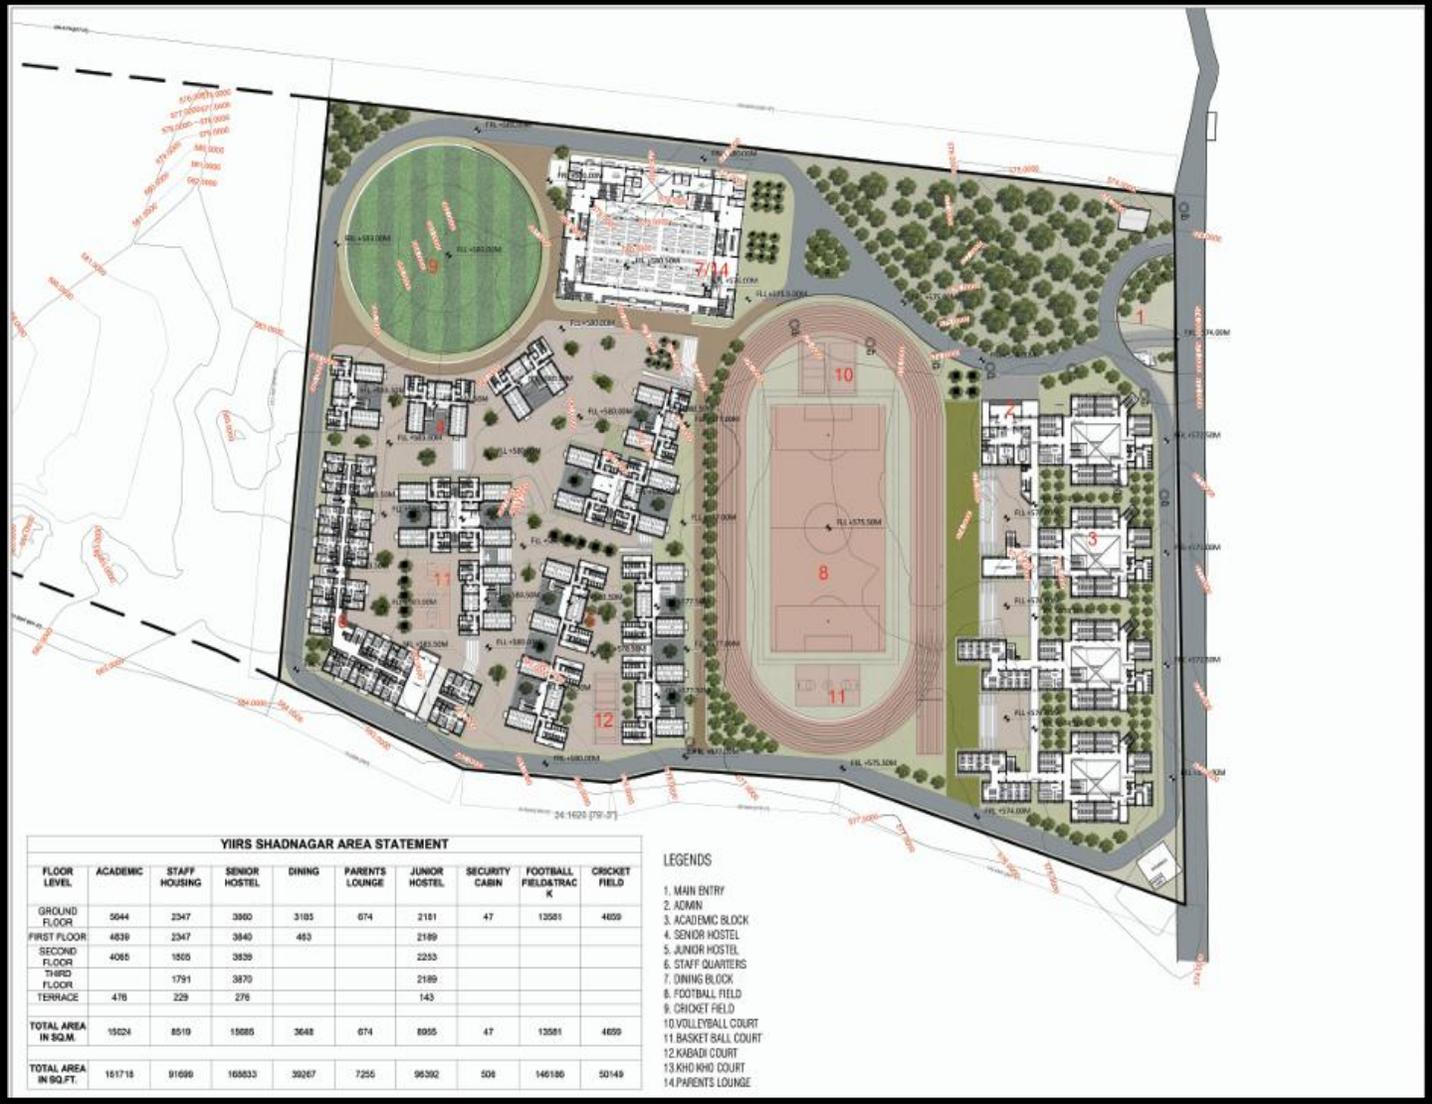

## STATUS OF YIIRS-SHADNAGAR

- Plinth Beam Work for Academic Building is in progress.
- Foundation Work for Senior and Junior Hostel Buildings are in progress.

### ACADEMIC BLOCK




### JUNIOR HOSTEL BLOCK



# STATUS OF YIIRS-KOLLAPUR

<b>Village</b>	Jatprole
<b>Mandal</b>	Pentlavelly
<b>District</b>	Nagarkurnool
<b>Survey No</b>	147, 508 & 177
<b>Land Extent</b>	Ac 21.55
<b>Contractor</b>	M/s. CH Gowri Shankar Infra Build India Pvt Ltd
<b>Consultant</b>	M/s. Architecture Paradigm

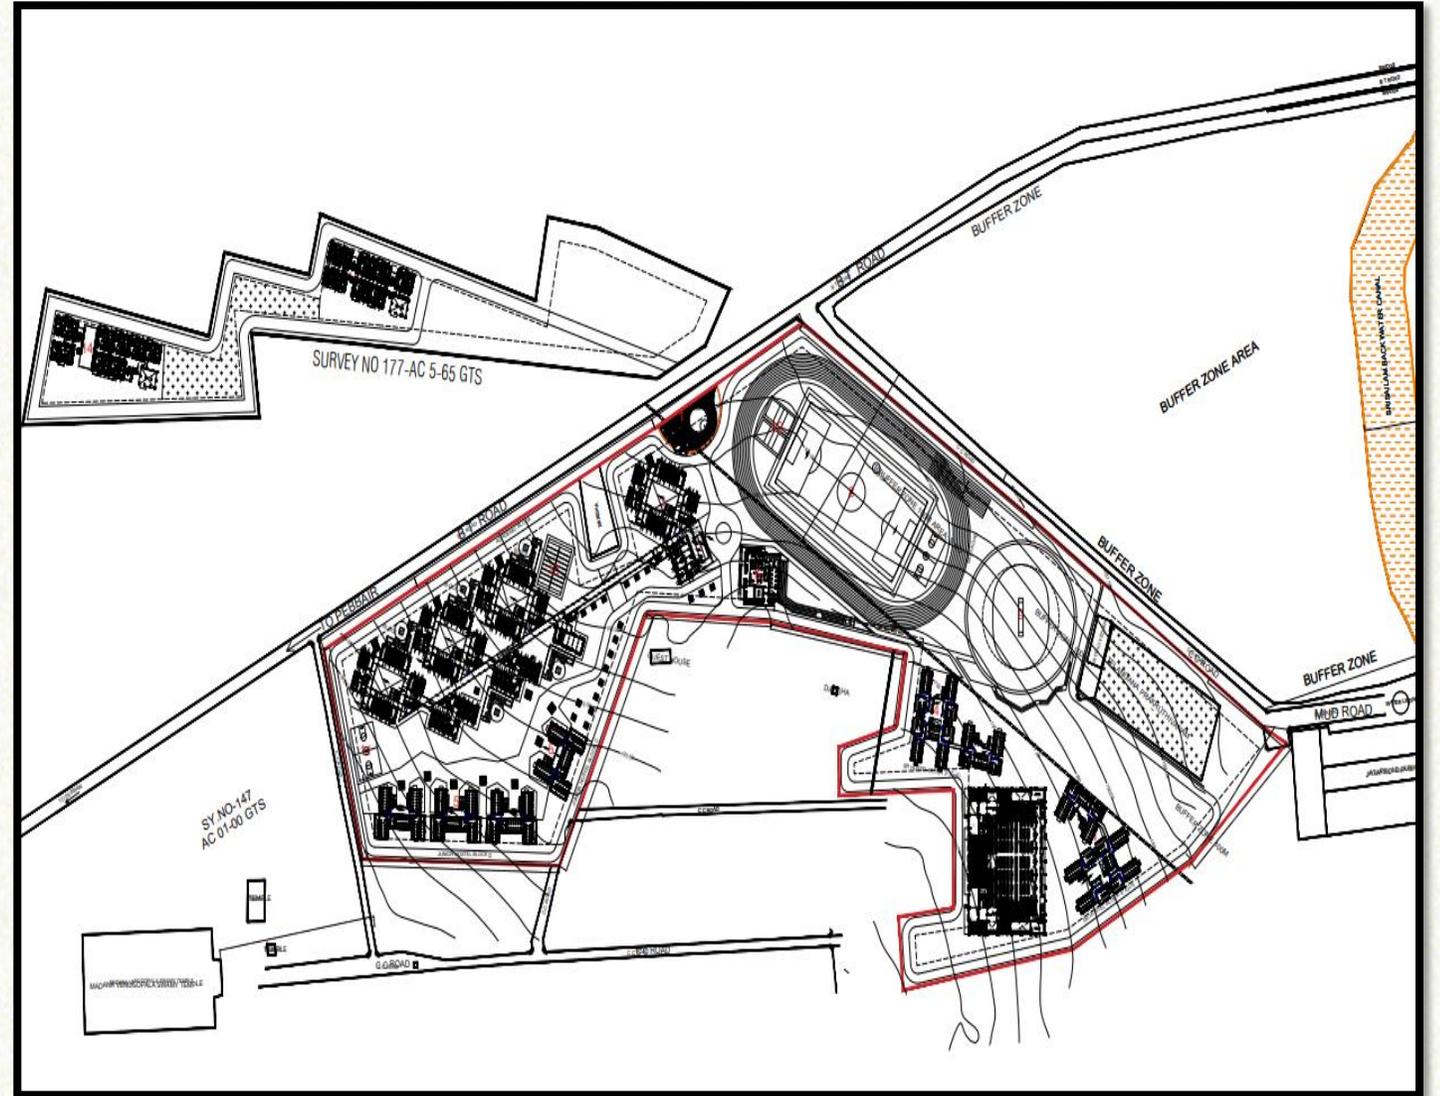

## STATUS OF YIIRS-KOLLAPUR

- Plinth Beam Work for Academic Building is in progress.
- Foundation Work for Junior Hostel Buildings is in progress.

### Junior Hostel



# STATUS OF YIIRS-NALGONDA

<b>Village</b>	Gandhamvari gudam
<b>Mandal</b>	Nalgonda
<b>District</b>	Nalgonda
<b>Survey No</b>	378,379, 380 & 384
<b>Land Extent</b>	Ac 25.0
<b>Contractor</b>	M/s. DJPR Construction Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-NALGONDA

- Plinth Beam Work for Academic Building is in progress.
- Foundation Work for Junior Hostel Buildings is in progress.

### Junior Hostel



# STATUS OF YIIRS-WARANGAL EAST

<b>Village</b>	Kothapet
<b>Mandal</b>	Warangal
<b>District</b>	Warangal
<b>Survey No</b>	298/2, 353/2,354/2, 355, 356, 357/2
<b>Land Extent</b>	Ac 18.2
<b>Contractor</b>	M/s. CH Gowri Shankar India Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-WARANGAL EAST

- Site mobilization activities are in Progress.



# STATUS OF YIIRS-MULUGU

<b>Village</b>	Incherla
<b>Mandal</b>	Mulugu
<b>District</b>	Mulugu
<b>Survey No</b>	17/1, 17/2, 17/3, 17/112 to 17/132
<b>Land Extent</b>	Ac 20.06
<b>Contractor</b>	M/s. Sudhakar Infratech Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-MULUGU

- Foundation work for Academic Building is in progress.

### ACADEMIC BLOCK



# STATUS OF YIIRS-KHAMMAM

<b>Village</b>	Raghunathapalem
<b>Mandal</b>	Raghunathapalem
<b>District</b>	Khammam
<b>Survey No</b>	218/1/P, 218/4/P, 218/5/P, 218/6/P, 218/8/P, 218/9(Full), 218/10(Full), 218/11/P& 218/12/P
<b>Land Extent</b>	AC.20.30
<b>Contractor</b>	M/s. SRR Projects Pvt. Ltd.
<b>Consultant</b>	M/s. Architecture Paradigm



## STATUS OF YIIRS-KHAMMAM

- Plinth Beam Work for Academic Building is in progress.
- Foundation Work for Senior and Junior Hostel Buildings are in progress.

### ACADEMIC BUILDING



### JUNIOR HOSTEL BLOCK



# STATUS OF YIIRS-PALAIR

<b>Village</b>	Thallampadu
<b>Mandal</b>	Khammam Rural
<b>District</b>	Khammam
<b>Survey No</b>	334/Part & 328/Part
<b>Land Extent</b>	Ac 21.0
<b>Contractor</b>	M/s. YRK Constructions
<b>Consultant</b>	M/s. Architecture Paradigm
<b>Site Issues</b>	Proposal is with the CCLA.



## STATUS OF YIIRS-PALAIR

- Site excavation work is in Progress.



# YIIRS ASIFABAD

<b>Village</b>	Indhani(v)
<b>Mandal</b>	Wankidi
<b>District</b>	Kumaram Bheem Asifabad
<b>Survey No</b>	321
<b>Land Extent</b>	Ac 15.00
<b>Contractor</b>	M/s. Vishwa Samudra Engineering Pvt Ltd
<b>Consultant</b>	M/s. Team One India



# YIIRS KHANAPUR

<b>Village</b>	Pulimadugu
<b>Mandal</b>	Utnoor
<b>District</b>	Nirmal
<b>Survey No</b>	41
<b>Land Extent</b>	Ac 25.00
<b>Contractor</b>	M/s. Vishwa Samudra Engineering Pvt Ltd
<b>Consultant</b>	M/s. Team One India



# YIIRS BELLAMPALLI

<b>Village</b>	Gurjal & Akenapally (v)
<b>Mandal</b>	Bellampalli
<b>District</b>	Mancherial
<b>Survey No</b>	4,5 & 394
<b>Land Extent</b>	Ac 25.00
<b>Contractor</b>	M/s. Vishwa Samudra Engineering Pvt Ltd
<b>Consultant</b>	M/s. Team One India



# YIIRS-MANCHERIAL

**Village** Rebbenapally  
**Mandal** Dandepally  
**District** Mancherial  
**Survey No** 521  
**Land Extent** Ac 21.63  
**Contractor** M/s Vishwa Samudra Engineering Pvt Ltd  
**Consultant** M/s. Team One India



# YIIRS-CHENNURU

<b>Village</b>	Somanpally
<b>Mandal</b>	Chennuru
<b>District</b>	Mancherial
<b>Survey No</b>	306
<b>Land Extent</b>	Ac 25
<b>Contractor</b>	M/s Vishwa Samudra Engineering Pvt Ltd
<b>Consultant</b>	M/s. Murty & Manyam



# YIIRS-PEDDAPALLE

<b>Village</b>	Rykaldevpalli
<b>Mandal</b>	Eligaid
<b>District</b>	Peddapalli
<b>Survey No</b>	Sy.No.514
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	M/s. M. Venkata Rao Infra Projects Pvt Ltd
<b>Consultant</b>	M/s. Murty & Manyam



# YIIRS-DHAMAPURI

<b>Village</b>	Nerella
<b>Mandal</b>	Dharmapuri
<b>District</b>	Jagtial
<b>Survey No</b>	Sy.No.263
<b>Land Extent</b>	Ac 25
<b>Contractor</b>	M/s M. Venkata Rao Infra Projects Pvt Ltd
<b>Consultant</b>	Murty & Manyam



# YIIRS-RAMAGUNDAM

<b>Village</b>	Ramagundam
<b>Mandal</b>	Ramagundam
<b>District</b>	Peddapalli
<b>Survey No</b>	Sy.No.366
<b>Land Extent</b>	Ac 26
<b>Contractor</b>	M/s M. Venkata Rao Infra Projects Pvt Ltd
<b>Consultant</b>	Murty & Manyam



# YIIRS-DEMULAWADA

<b>Village</b>	Tettakunta
<b>Mandal</b>	Vemulwada
<b>District</b>	Rajanna Sircilla
<b>Survey No</b>	Sy.No
<b>Land Extent</b>	Ac 22
<b>Consultant</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Contractor</b>	M/s. FORM'D Architecture Interior Design
<b>Site Issues</b>	Allotted site is not feasible. Alternate site is requested.

# YIIRS-CHOPPADANDI

<b>Village</b>	Rukmapur
<b>Mandal</b>	Choppadandi
<b>District</b>	Karimnagar
<b>Survey No</b>	Sy.No.112
<b>Land Extent</b>	Ac 20.25
<b>Consultant</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Contractor</b>	M/s. FORM'D Architecture Interior Design



# YIIRS-MANAKONDUR

<b>Village</b>	Yadavullapalli
<b>Mandal</b>	Thimmapur
<b>District</b>	Karimnagar
<b>Survey No</b>	Sy.No. :502,520,522
<b>Land Extent</b>	Ac 20
<b>Consultant</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Contractor</b>	M/s. FORM'D Architecture Interior Design



# YIIRS-JAGTIAL

<b>Village</b>	Chalgal
<b>Mandal</b>	Jagtial Rural
<b>District</b>	Jagtial
<b>Survey No</b>	Sy.No. :502,520,522
<b>Land Extent</b>	Ac 25
<b>Consultant</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Contractor</b>	M/s. FORM'D Architecture Interior Design
<b>Site Issues</b>	WALAMTARI has not accepted the proposal for transfer of the land. Therefore, an alternative site or consent from WALAMTARI is required.



# YIIRS-ARMUR

**Village** Ankapur  
**Mandal** Armur  
**District** Nizamabad  
**Survey No** 493/1  
**Land Extent** Ac 20.07  
**Consultant** M/s. Anusha Projects Pvt Ltd  
**Contractor** M/s. Varma Consultancy



# YIIRS-BODHAN

**Village**

Bodhan

**Mandal**

Armur

**District**

Nizamabad

**Survey No**

Sy.No.979

**Land Extent**

Ac 27.10

**Contractor**


M/s. Anusha Projects Pvt Ltd

**Consultant**

M/s. Varma Consultancy

**Site Issues**

Proposal is with the CCLA.

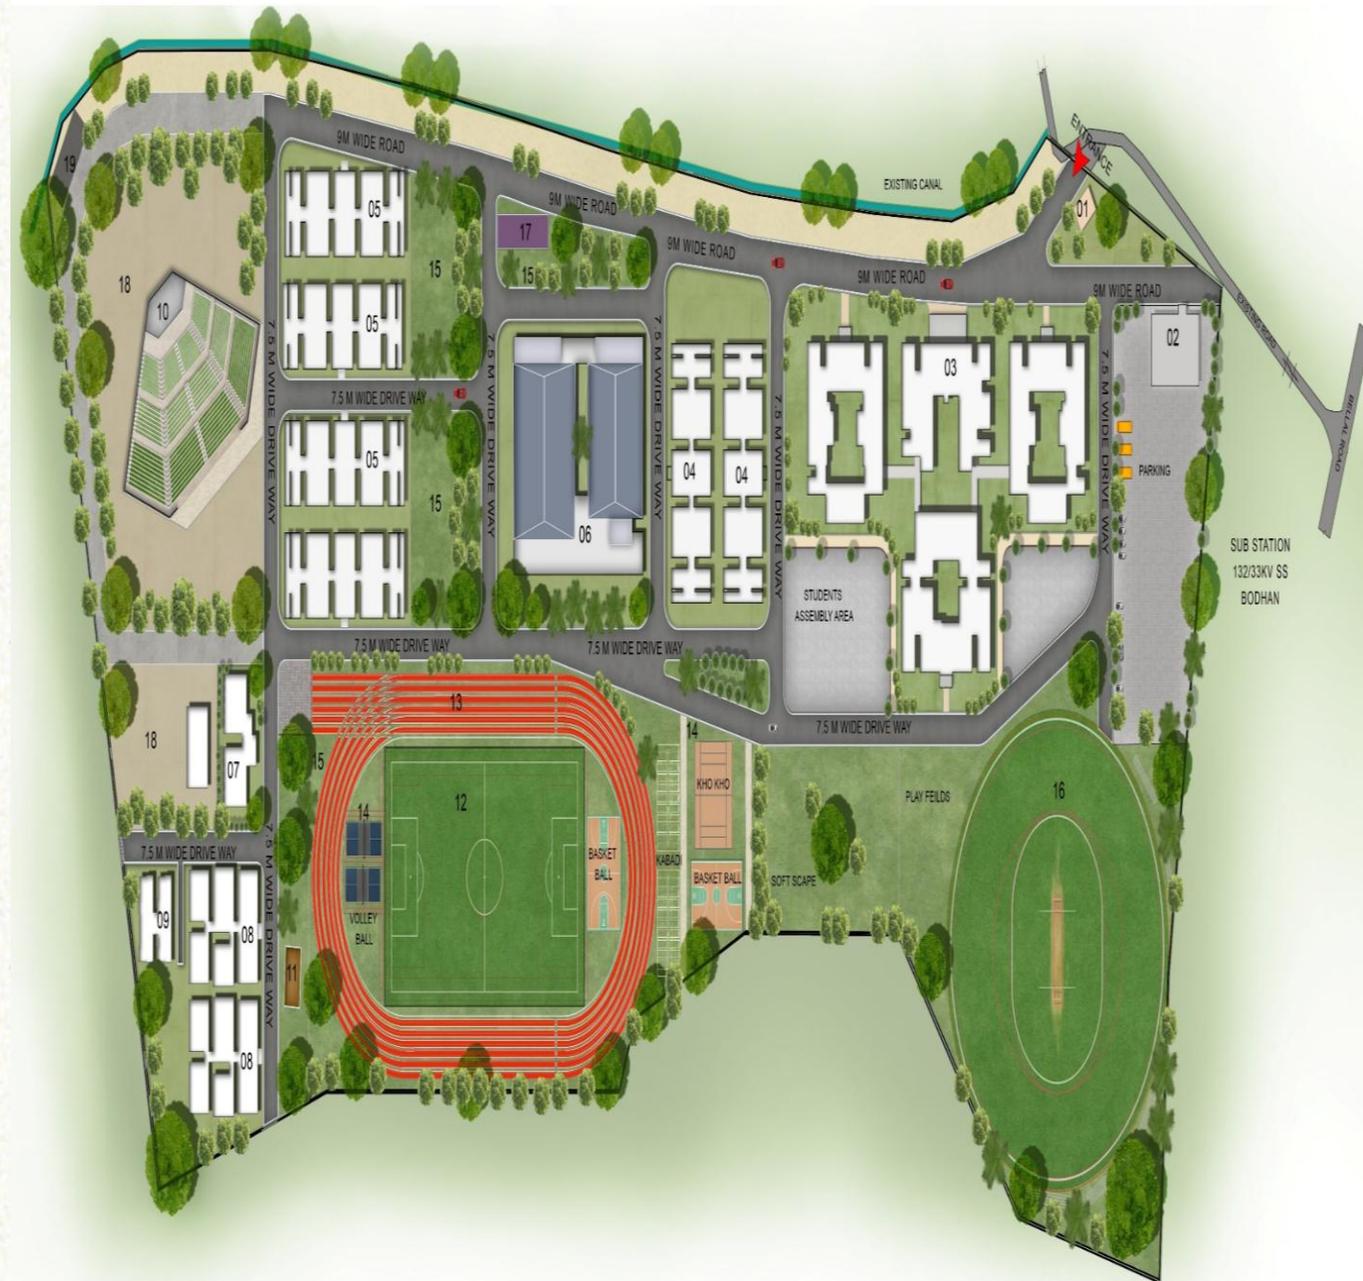

# YIIRS- NIZAMABAD (RURAL)

<b>Village</b>	Suddulam
<b>Mandal</b>	Dichpally
<b>District</b>	Nizamabad
<b>Survey No</b>	Sy.No.233/1, 371, 372, 379
<b>Land Extent</b>	20 Acres 27.2 Guntas
<b>Contractor</b>	M/s. Anusha Projects Pvt Ltd
<b>Consultant</b>	M/s. Varma Consultancy
<b>Site Issues</b>	Proposal is with the CCLA.




# YIIRS-JUKKAL

<b>Village</b>	Madnoor
<b>Mandal</b>	Madnoor
<b>District</b>	Kamareddy
<b>Survey No</b>	Sy.No 499
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	Tracks and Towers Infratech Pvt Ltd
<b>Consultant</b>	Satyavani Projects



LEGEND		
1. ACADEMIC&ADMIN BLOCK	7. 1 BHK QUARTERS	13. FOOTBALL GROUND
2. JUNIOR DORMITORY	8. SECURITY BLOCK	14. CRICKET GROUND
3. SENIOR DORMITORY	9. CLINIC & PARENT'S WAITING LOUNGE	15. OPEN SPACE
4. KITCHEN CUM DINING & INDOOR GAMES	10. STP	16. OPEN AIR THEATRE
5. 3 BHK QUARTERS	11. WATER SUMP (400CUM)	17. PARKING
6. 2 BHK QUARTERS	12. ELECTRICAL YARD	



# YIIRS-BANSWADA

<b>Village</b>	Banswada
<b>Mandal</b>	Banswada
<b>District</b>	Nizamabad
<b>Survey No</b>	Sy.No 365/1
<b>Land Extent</b>	Ac 15
<b>Contractor</b>	Tracks and Towers Infratech Pvt Ltd
<b>Consultant</b>	Satyavani Projects



# YIIRS-YELLAREDDY

<b>Village</b>	Mothe
<b>Mandal</b>	Lingampet
<b>District</b>	Kamareddy
<b>Survey No</b>	Sy.No 164
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	Tracks and Towers Infratech Pvt Ltd
<b>Consultant</b>	Satyavani Projects
<b>Site Issues</b>	Proposal is with the CCLA.







# YIIRS-PATANCHERU

<b>Village</b>	Ameenpur
<b>Mandal</b>	Ameenpur
<b>District</b>	Sangareddy
<b>Survey No</b>	Sy. No. 993
<b>Land Extent</b>	Ac 15
<b>Contractor</b>	M/s. Megha Engineering and Infrastructure Ltd
<b>Consultant</b>	M/s. OCI Architects
<b>Site Issues</b>	Originally identified site is not Feasible. Alternate site is requested.

# YIIRS-STATION GHANPUR

<b>Village</b>	Konnaichalam
<b>Mandal</b>	Zafarghad
<b>District</b>	Jangaon
<b>Survey No</b>	Sy. No. 161/C/2
<b>Land Extent</b>	Ac 21
<b>Contractor</b>	M/s. Inderjit Mehta Constructions Pvt Ltd
<b>Consultant</b>	M/s. Young Designers



# YIIRS-PARAKALA

<b>Village</b>	Rajipet
<b>Mandal</b>	Parakala
<b>District</b>	Warangal Rural
<b>Survey No</b>	Sy.No 18 & 19
<b>Land Extent</b>	Ac 21.35
<b>Contractor</b>	M/s. Inderjit Mehta Constructions Pvt Ltd
<b>Consultant</b>	M/s. Young Designers
<b>Site Issues</b>	Housing department NOC is required.



# YIIRS-PALAKURTHY

**Village** Kodakandla  
**Mandal** Kodakandla  
**District** Jangaon  
**Survey No** Sy.No 100  
**Land Extent** Ac 23  
**Contractor** M/s. Inderjit Mehta  
 Constructions Pvt Ltd  
**Consultant** M/s. Young Designers



# YIIRS-WARDHANNAPET

<b>Village</b>	Kokirala
<b>Mandal</b>	Inavole
<b>District</b>	Warangal Urban
<b>Survey No</b>	Sy.No 528
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	M/s. Inderjit Mehta Constructions Pvt Ltd
<b>Consultant</b>	M/s. Young Designers




# YIIRS-WARANGAL WEST

**Village** Pegadapally  
**Mandal** Hasanparthy  
**District** Warangal Urban  
**Survey No** Sy. No. 101, 132/1,  
142/1, 143, 144,  
145, 193  
**Land Extent** Ac 20  
**Contractor** M/s. Inderjit Mehta  
Constructions Pvt Ltd  
**Consultant** M/s. Young Designers  
**Site Issues** Proposal is with the  
CCLA.




# YIIRS- BHUPALPALLE

**Village** Mylaram  
**Mandal** Ghanpur Mulugu  
**District** Jayashankar Bhupalpalle  
**Survey No** 205  
**Land Extent** Ac 40.115  
**Contractor** M/s KMV Projects  
**Consultant** M/s. Mukesh & Associates  
**Site Issues** Proposal is with the CCLA.

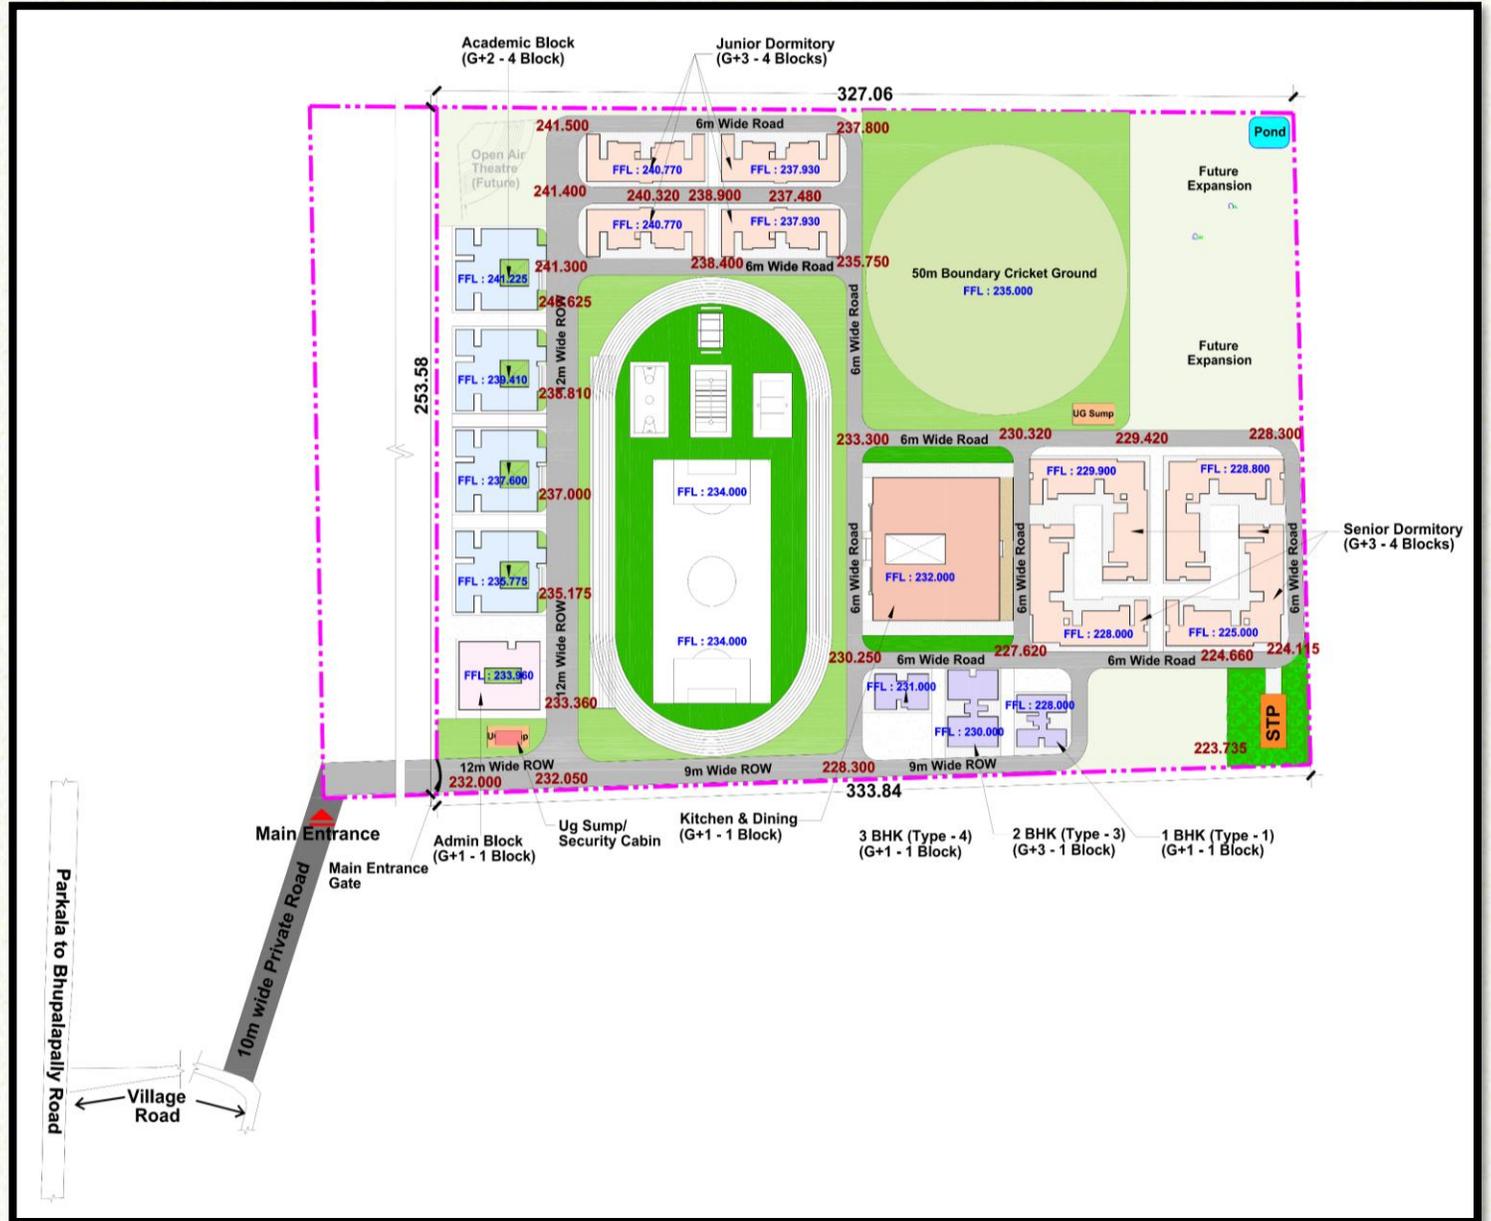


# YIIRS-NARSAMPET

**Village** Ameenabad  
**Mandal** Chennaraopet  
**District** Warangal Rural  
**Survey No** Sy. No. 2082, 2122, 2127, 2128, 2131 & 2133  
**Land Extent** Ac 31.08  
**Contractor** M/s KMV Projects  
**Consultant** M/s. Mukesh & Associates  
**Site Issues** Proposal is with the CCLA.

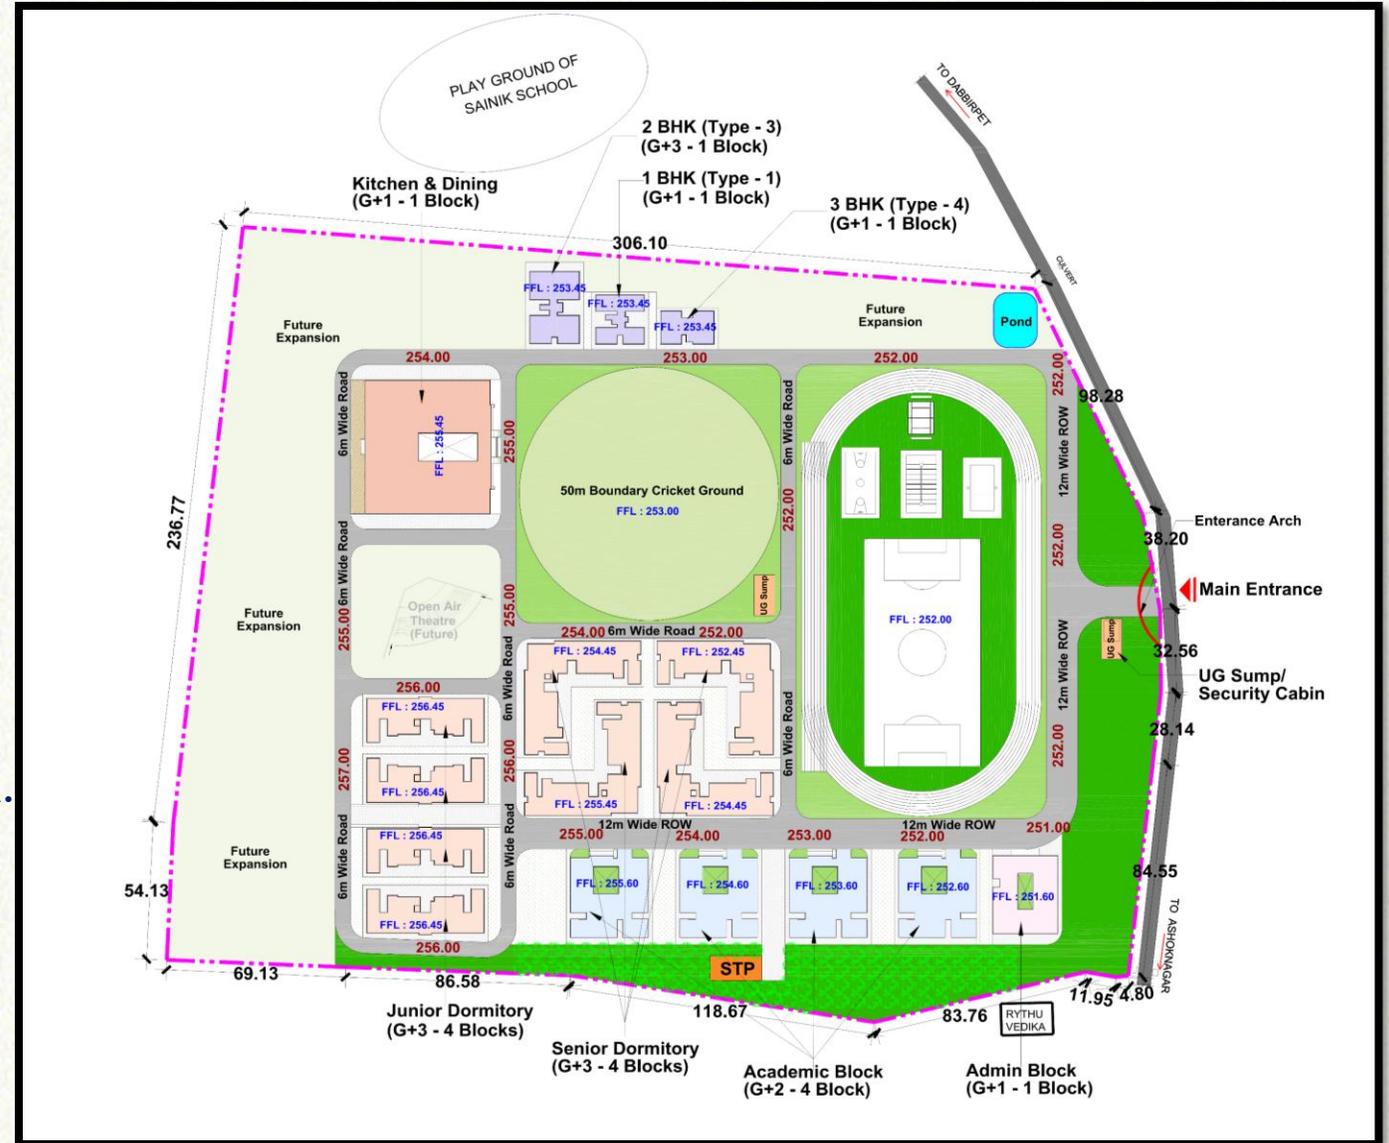


# YIIRS-MAHABUBABAD

**Village** Boddugonda  
**Mandal** Gudur  
**District** Warangal Rural  
**Survey No** Sy. No. 200  
**Land Extent** Ac 26  
**Contractor** M/s. KMV Projects  
**Consultant** M/s. Mukesh & Associates

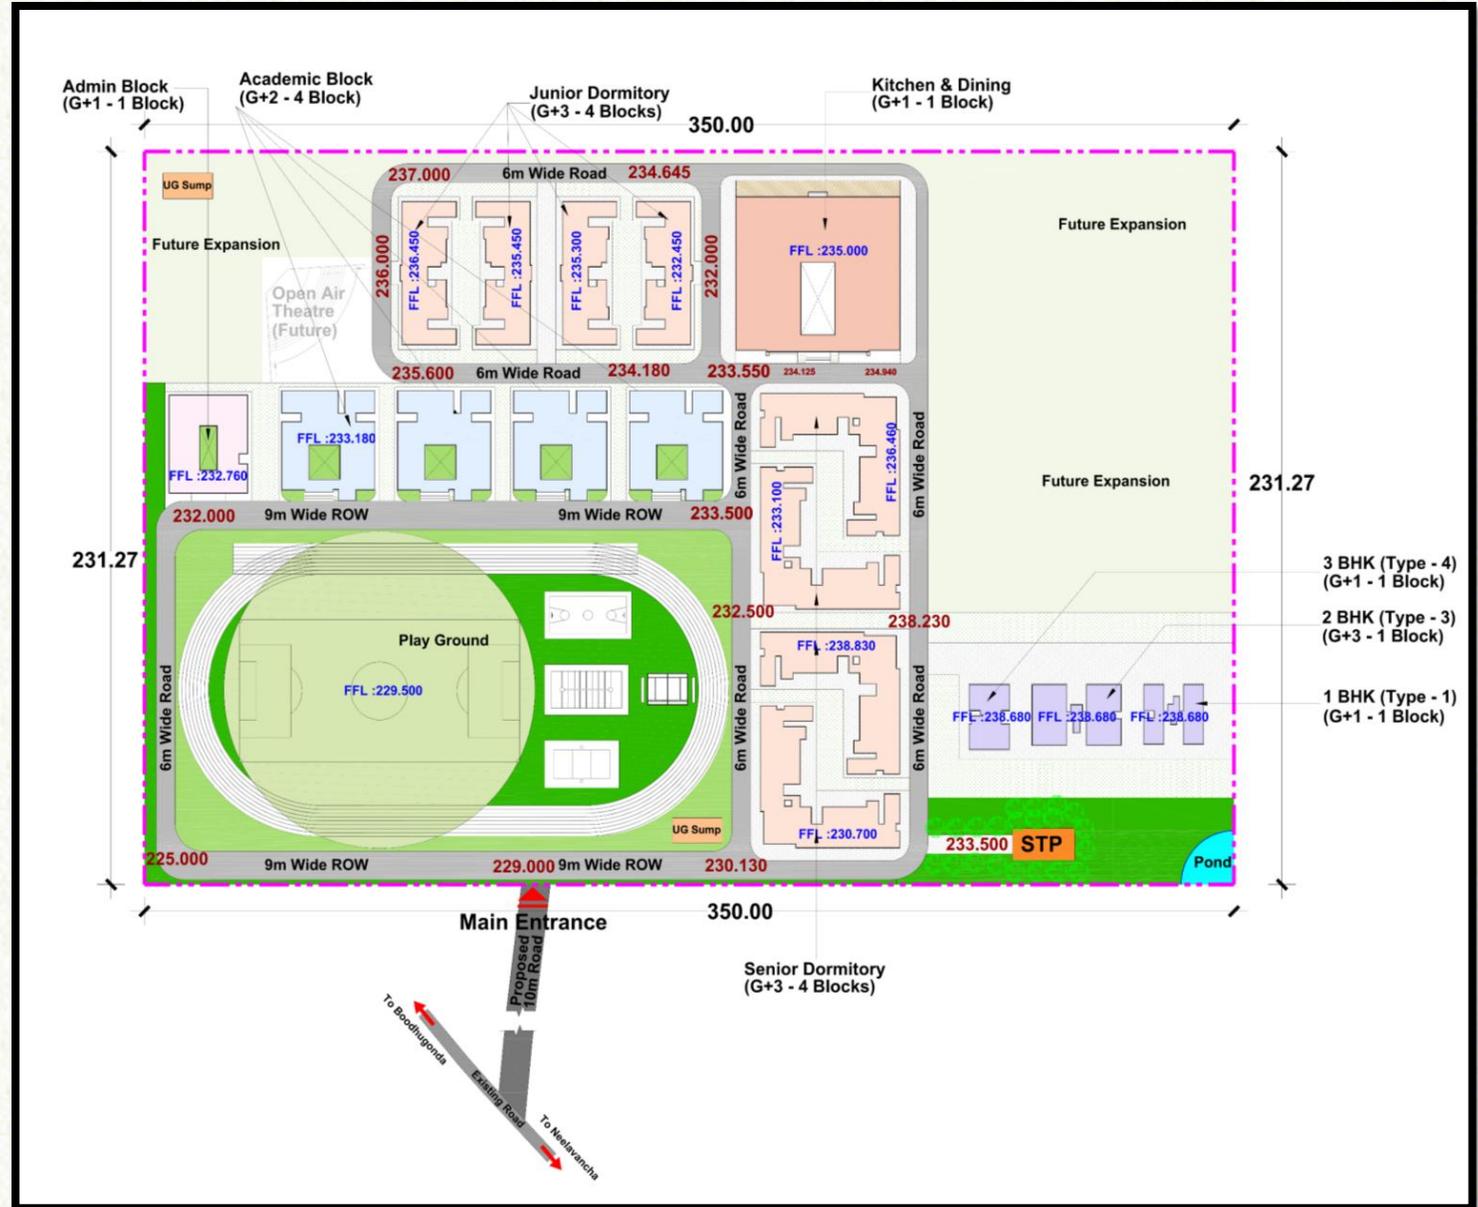

# YIIRS-DORNAKAL

**Village** Ayyavaripalli  
**Mandal** Kuravi  
**District** Mahabubabad  
**Survey No** Sy. No. 285/1  
**Land Extent** Ac 20  
**Contractor** M/s KMV Projects  
**Consultant** M/s. Mukesh & Associates

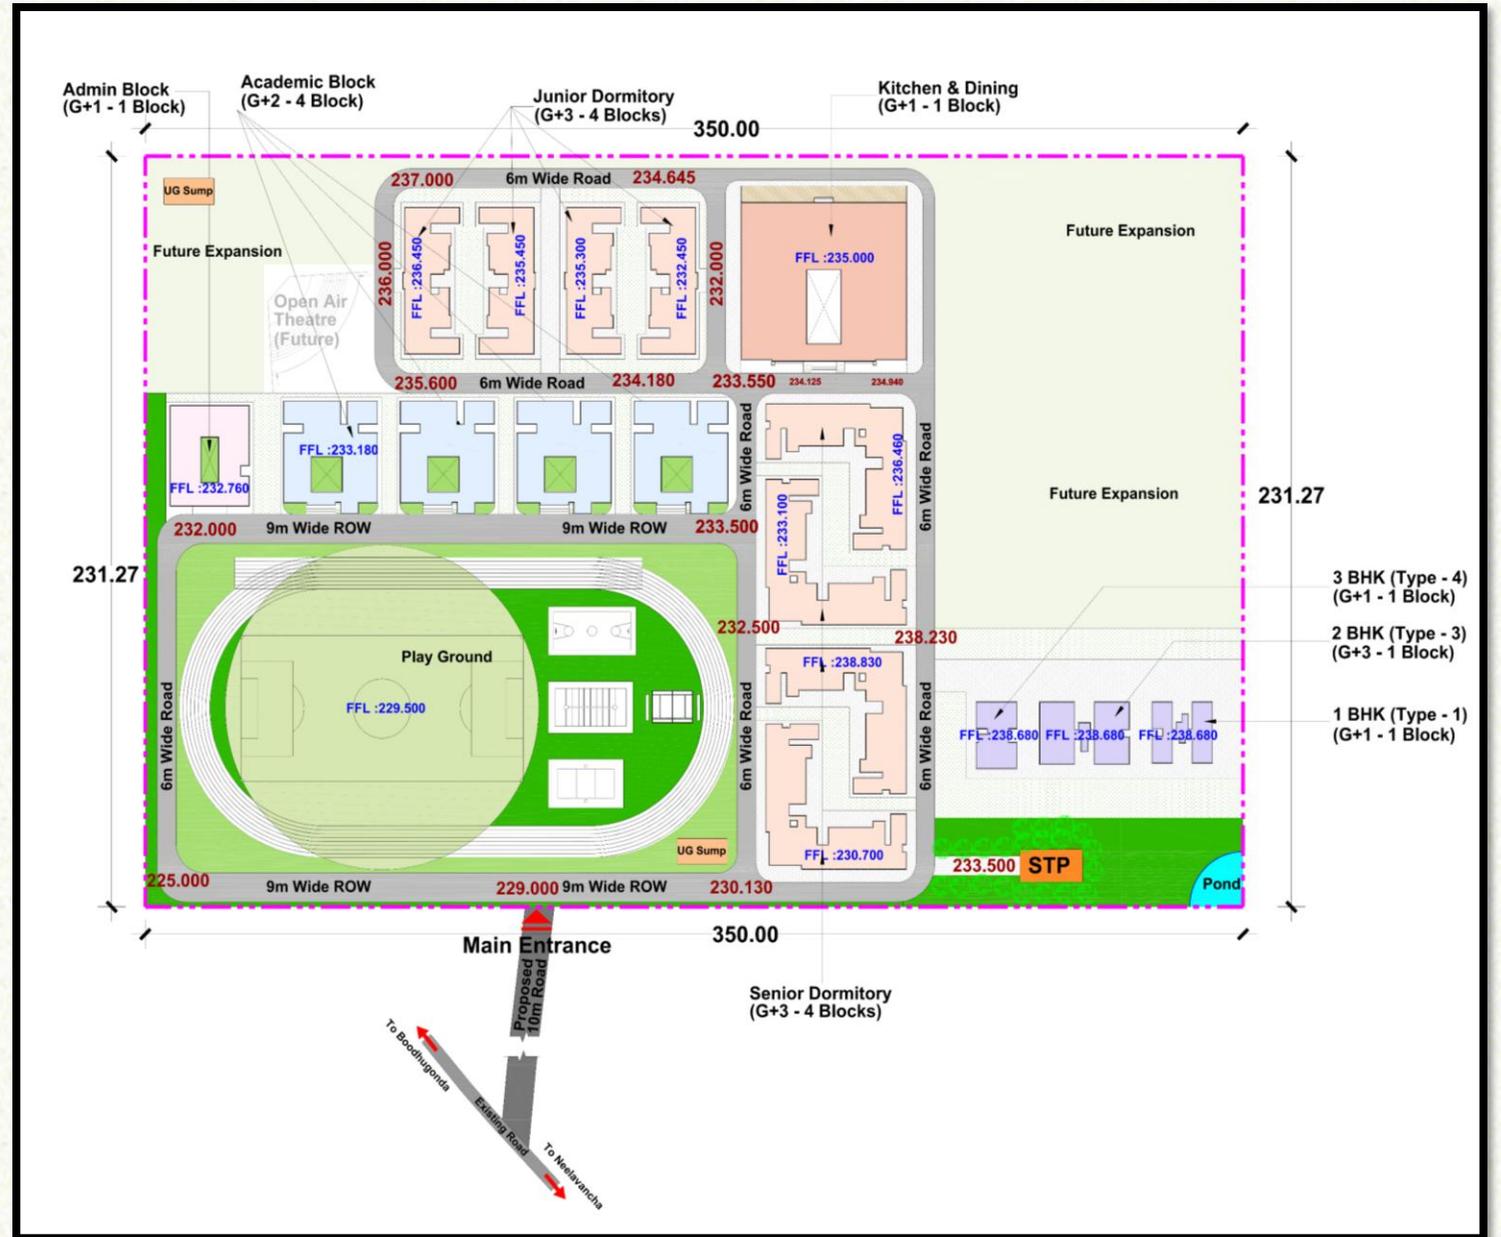

# YIIRS-PINAPAKA


<b>Village</b>	Manuguru
<b>Mandal</b>	Manuguru
<b>District</b>	Bhadradi
<b>Survey No</b>	Sy.No 138/1/2
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	M/s. SRR Projects Pvt Ltd
<b>Consultant</b>	M/s. Enarch





# YIIRS-BHADRACHALAM

<b>Village</b>	Peddanalaballi
<b>Mandal</b>	Dummugudem
<b>District</b>	Bhadradi
<b>Survey No</b>	Sy.No.394, 4&5
<b>Land Extent</b>	Ac 20.75
<b>Contractor</b>	M/s. SRR Projects Pvt Ltd
<b>Consultant</b>	M/s. Enarch

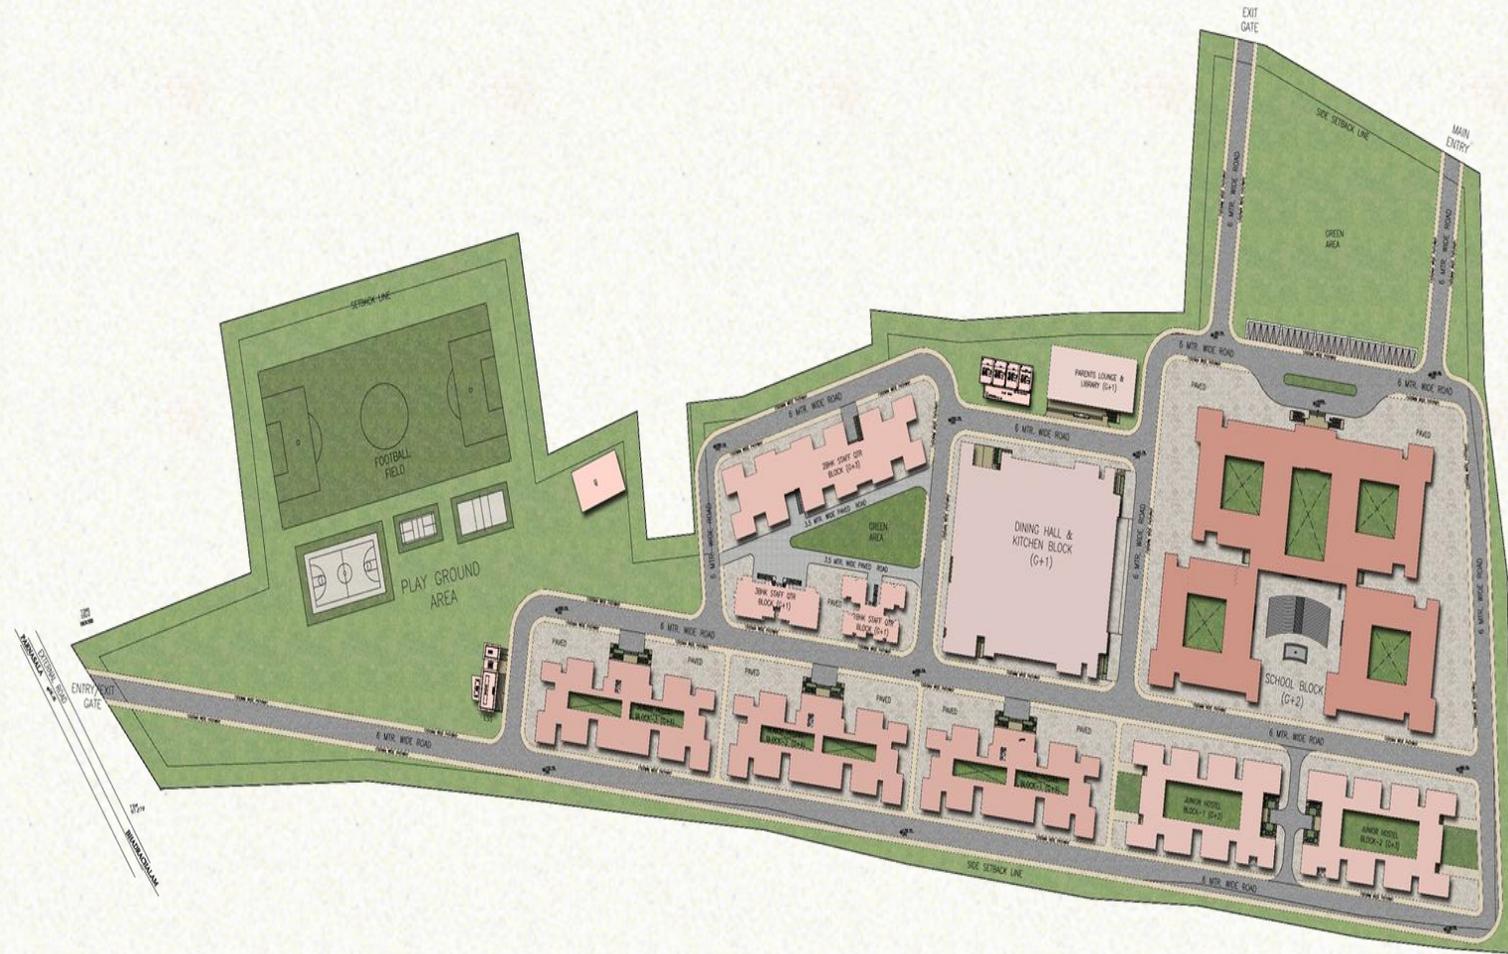

# YIIRS-ASWARAOPETA

<b>Village</b>	Nacharam
<b>Mandal</b>	Dammapeta
<b>District</b>	Bhadradi
<b>Survey No</b>	Sy.No.493
<b>Land Extent</b>	Ac 21.25
<b>Contractor</b>	M/s. BSR Infratech India Ltd
<b>Consultant</b>	M/s. Silparupa Consultants
<b>Site Issues</b>	Sericulture Dept. NOC required.





# YIIRS-SATHUPALLE

<b>Village</b>	Bethupalli
<b>Mandal</b>	Sathupalli
<b>District</b>	Khammam
<b>Survey No</b>	Sy.No.40/Part
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	M/s. BSR Infratech India Ltd
<b>Consultant</b>	M/s. Silparupa Consultants
<b>Site Issues</b>	Proposal is with the CCLA.



# YIIRS-WYRA

<b>Village</b>	Wyra
<b>Mandal</b>	Brahmanapally
<b>District</b>	Khammam
<b>Survey No</b>	Sy.No. 106, 108, 209 & 210
<b>Land Extent</b>	Ac 13.4
<b>Contractor</b>	M/s. BSR Infratech India Ltd
<b>Consultant</b>	M/s. Silparupa Consultants



# YIIRS-KODAD

Village

Chilkuru

Mandal

Chilkuru

District

Suryapet

Survey No

Sy.No 1151

Land Extent


Ac 22

Contractor

M/s Megha Engineering and Infrastructure Ltd


Consultant

M/s. Sri Harsha

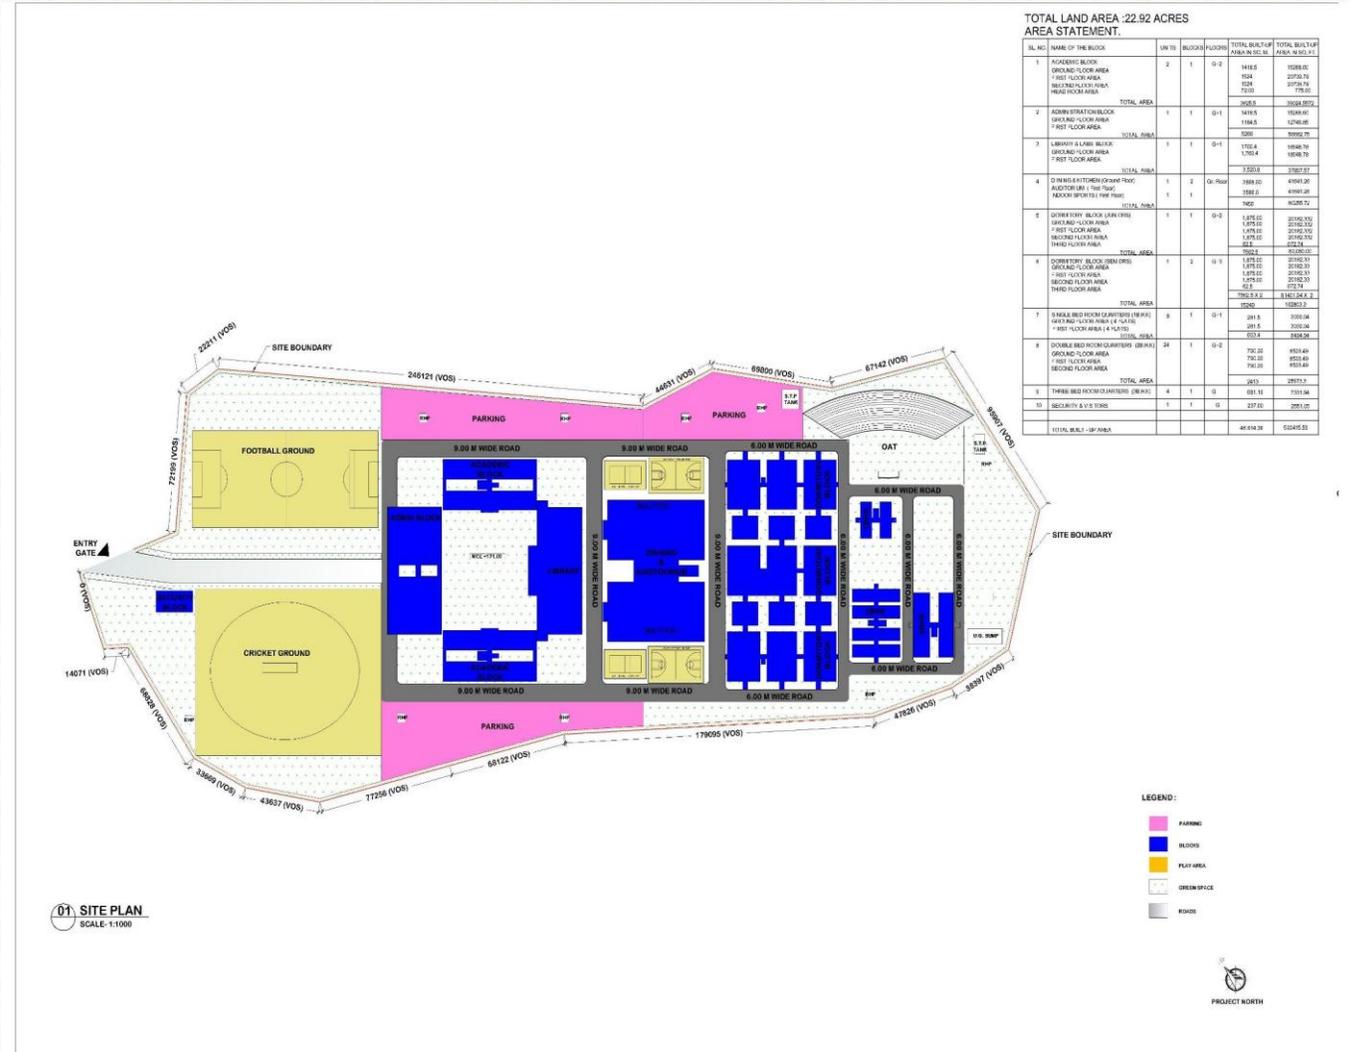

# YIIRS-MIRYALAGUDA


<b>Village</b>	Miryalaguda
<b>Mandal</b>	Chilkuru
<b>District</b>	Nalgonda
<b>Survey No</b>	Sy.No 214
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Consultant</b>	M/s. Sri Harsha
<b>Site Issues</b>	Proposal is with the CCLA.

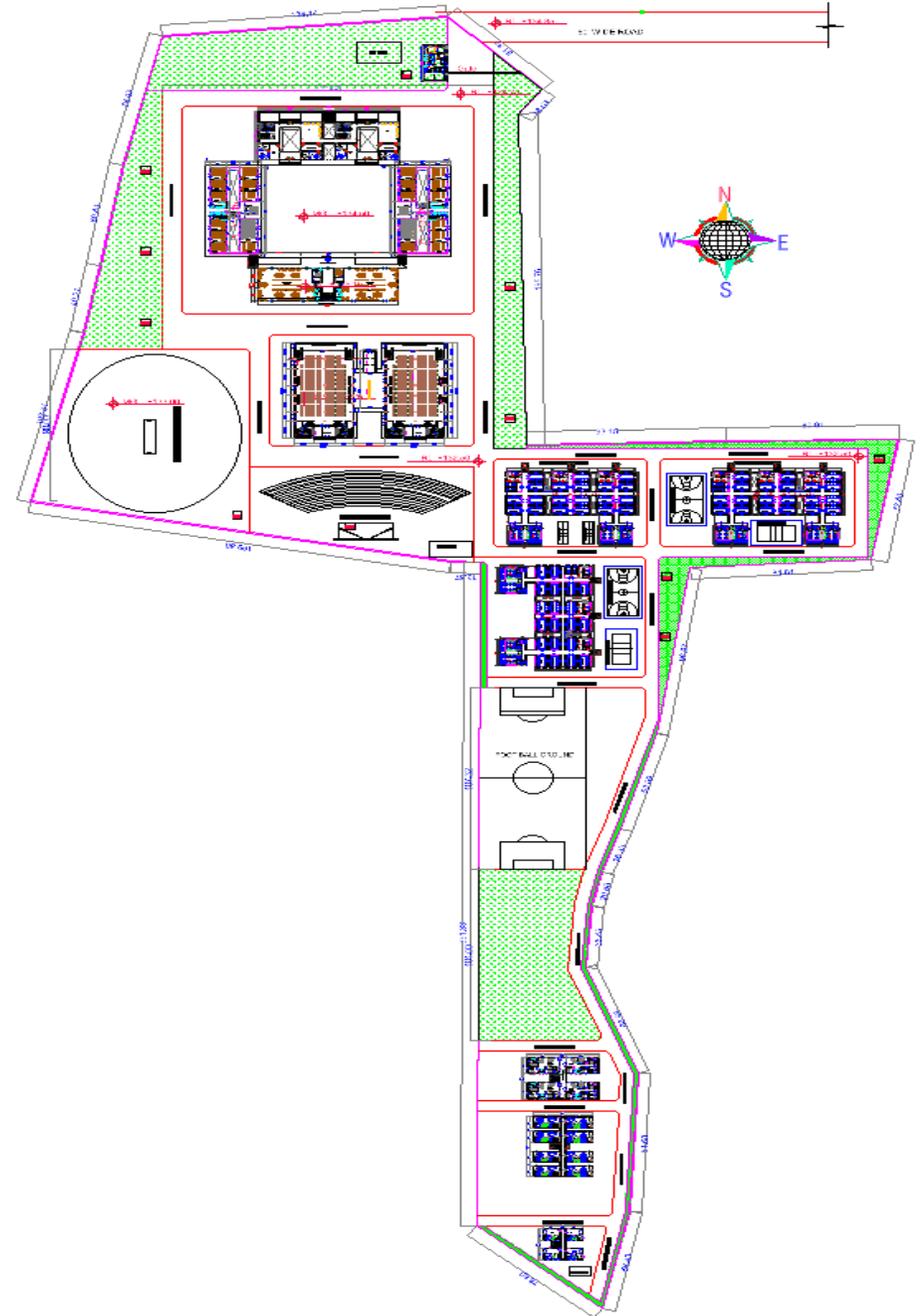

# YIIRS-NAGARJUNASAGAR

**Village**  
**Mandal**  
**District**  
**Survey No**  
**Land Extent**  
**Contractor**  
**Consultant**  
**Site Issues**


Chalukurthy  
 Peddavoora  
 Nalgonda  
 Sy.No 48,49,52 to 56 , 58,279 to 282, 366 to 371, 376,377  
 Ac 20.02  
 M/s Megha Engineering and Infrastructure Ltd  
 M/s. Sri Harsha  
 Proposal is with the CCLA.

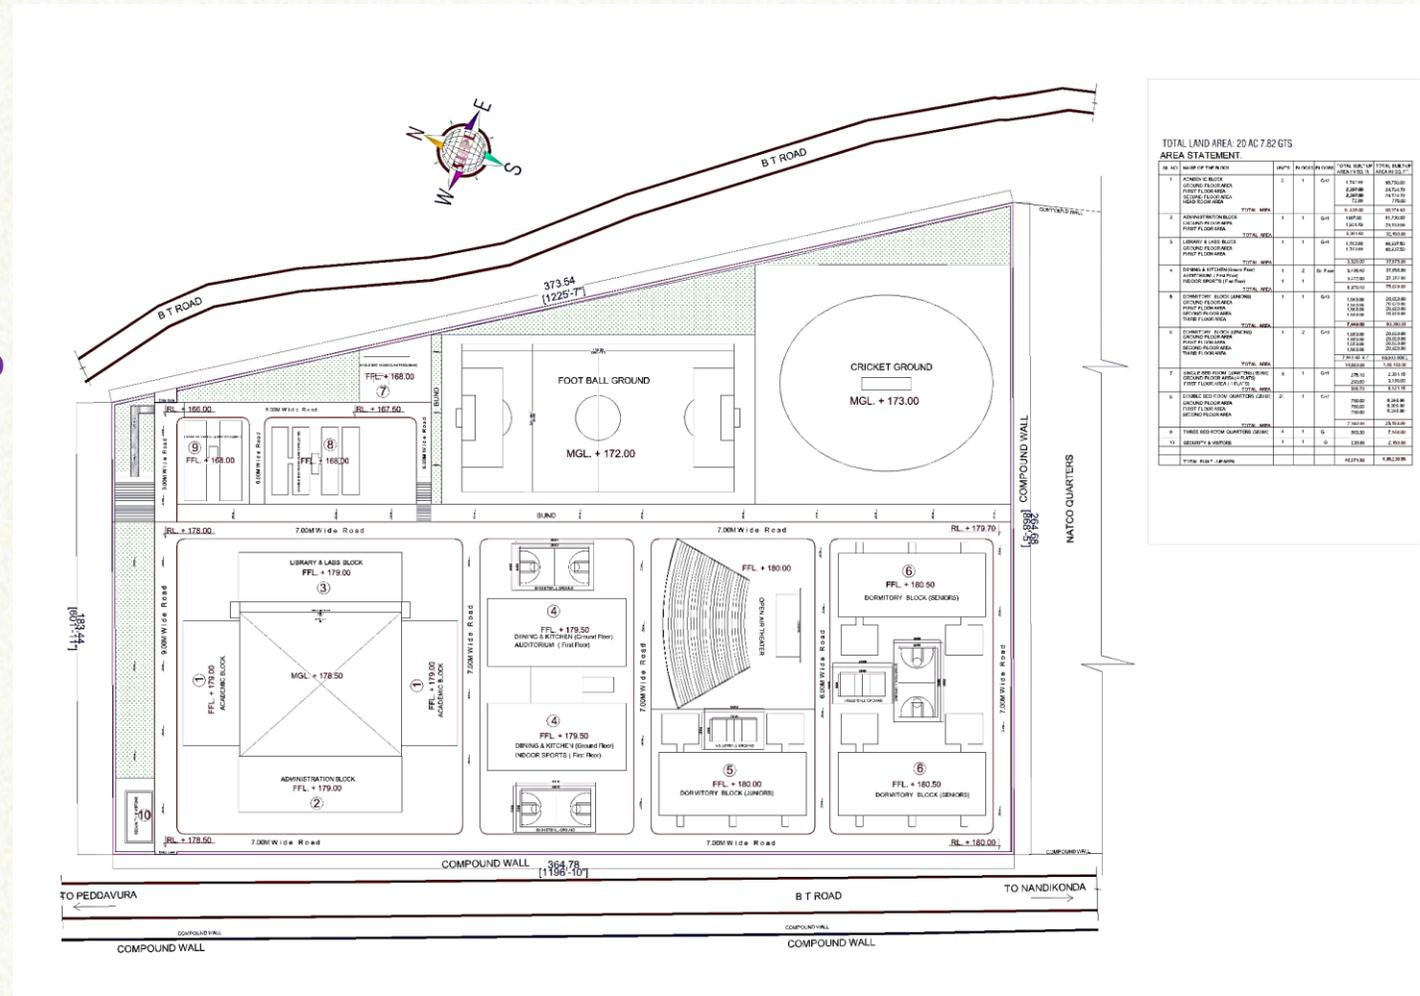



# YIIRS-ALAIR

<b>Village</b>	Mulkapalli
<b>Mandal</b>	Thurkapalli
<b>District</b>	Yadadri Bhongiri
<b>Survey No</b>	Sy.No.92/1
<b>Land Extent</b>	Ac 20.07
<b>Contractor</b>	M/s Everest Infra Ventures Pvt Ltd
<b>Consultant</b>	M/s. SS Infrastructure Project consultants Pvt Ltd.

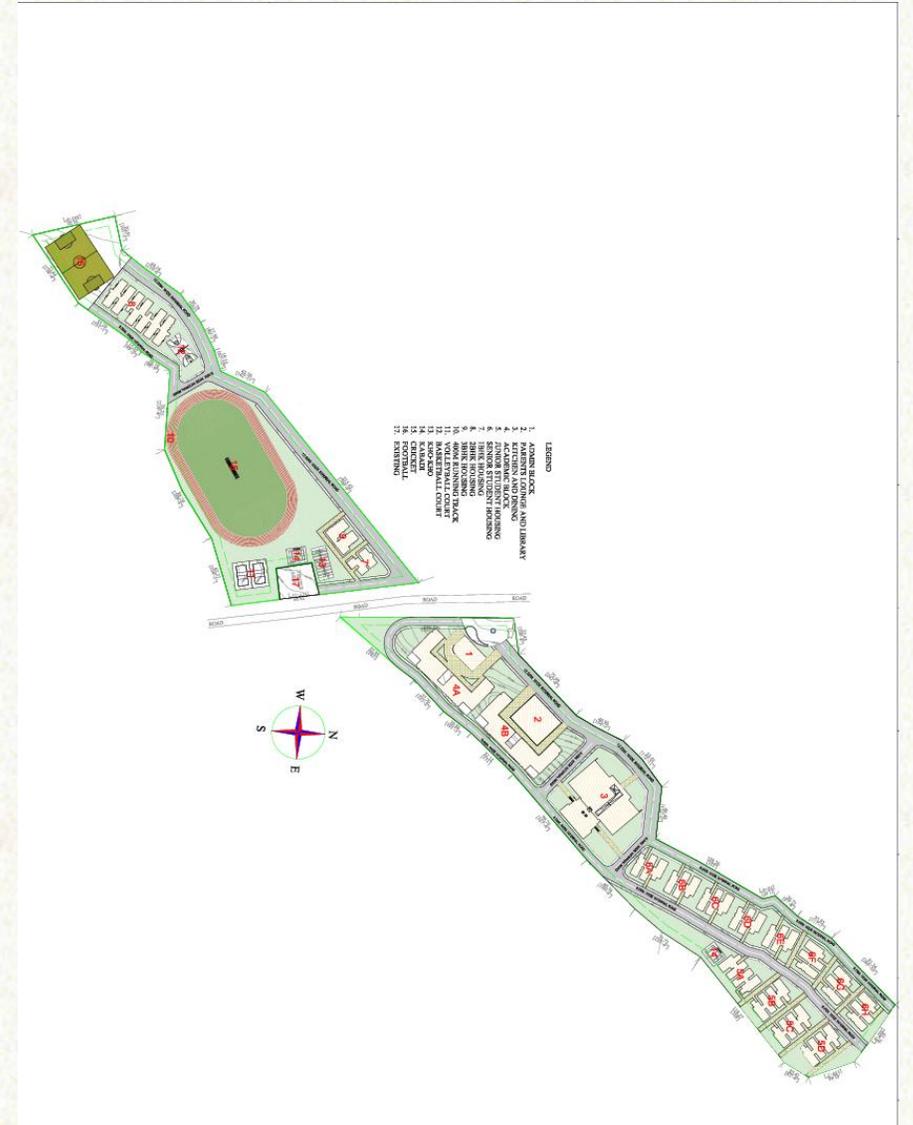



# YIIRS- MUNUGODE

<b>Village</b>	Kalwakuntla
<b>Mandal</b>	Munugodu
<b>District</b>	Nalgonda
<b>Survey No</b>	Sy.No.58
<b>Land Extent</b>	Ac 22.3
<b>Contractor</b>	M/s. Everest Infra Ventures Pvt Ltd
<b>Consultant</b>	M/s. SS Infrastructure Project consultants Pvt Ltd.



# YIIRS- NAKREKAL

<b>Village</b>	Nakrekal
<b>Mandal</b>	Munugodu
<b>District</b>	Nalgonda
<b>Survey No</b>	Sy. No. 423 to 427
<b>Land Extent</b>	Ac 20.3
<b>Contractor</b>	M/s Everest Infra Ventures Pvt Ltd
<b>Consultant</b>	M/s. SS Infrastructure Project consultants Pvt Ltd.
<b>Site Issues</b>	Proposal is with the CCLA.



# YIIRS- THUNGATHURTHI

<b>Village</b>	Thirumalagiri Thonda
<b>Mandal</b>	Thirumalagiri
<b>District</b>	Suryapet
<b>Survey No</b>	Sy. No. 98
<b>Land Extent</b>	Ac 20.1
<b>Contractor</b>	M/s. Everest Infra Ventures Pvt Ltd
<b>Consultant</b>	M/s. SS Infrastructure Project consultants Pvt Ltd.




# YIIRS- MEDCHAL

<b>Village</b>	Aithepally
<b>Mandal</b>	Kapra
<b>District</b>	Medchal Malkajgiri
<b>Survey No</b>	Sy.No.706/P
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	
<b>Consultant</b>	M/s. Matrix Consultants




# YIIRS- IBRAHIMPATNAM

<b>Village</b>	Mazeedpur
<b>Mandal</b>	Abdullapurmet
<b>District</b>	Rangareddy
<b>Survey No</b>	Sy.No.57
<b>Land Extent</b>	Ac 40.9
<b>Contractor</b>	
<b>Consultant</b>	Matrix Consultants
<b>Site Issues</b>	Proposal is with the CCLA.

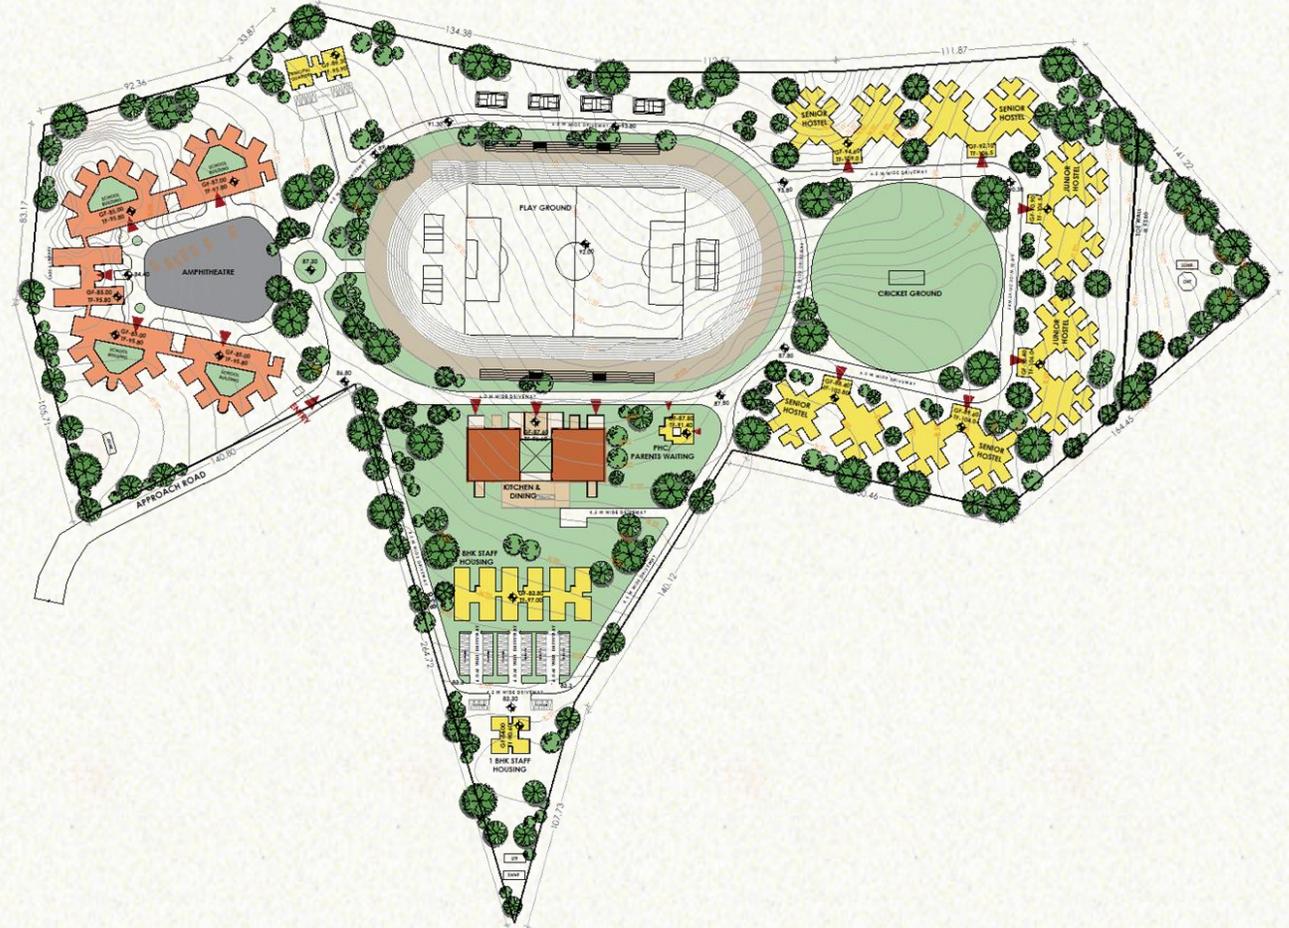


# YIIRS-CHEVELLA

**Village** Pasmamula  
**Mandal** Abdullapurmet  
**District** Rangareddy  
**Survey No** Sy.No.  
**Land Extent** Ac 20  
**Contractor**  
**Consultant** M/s Usha Reddy Consultants  
**Site Issues** Proposal is with the CCLA.

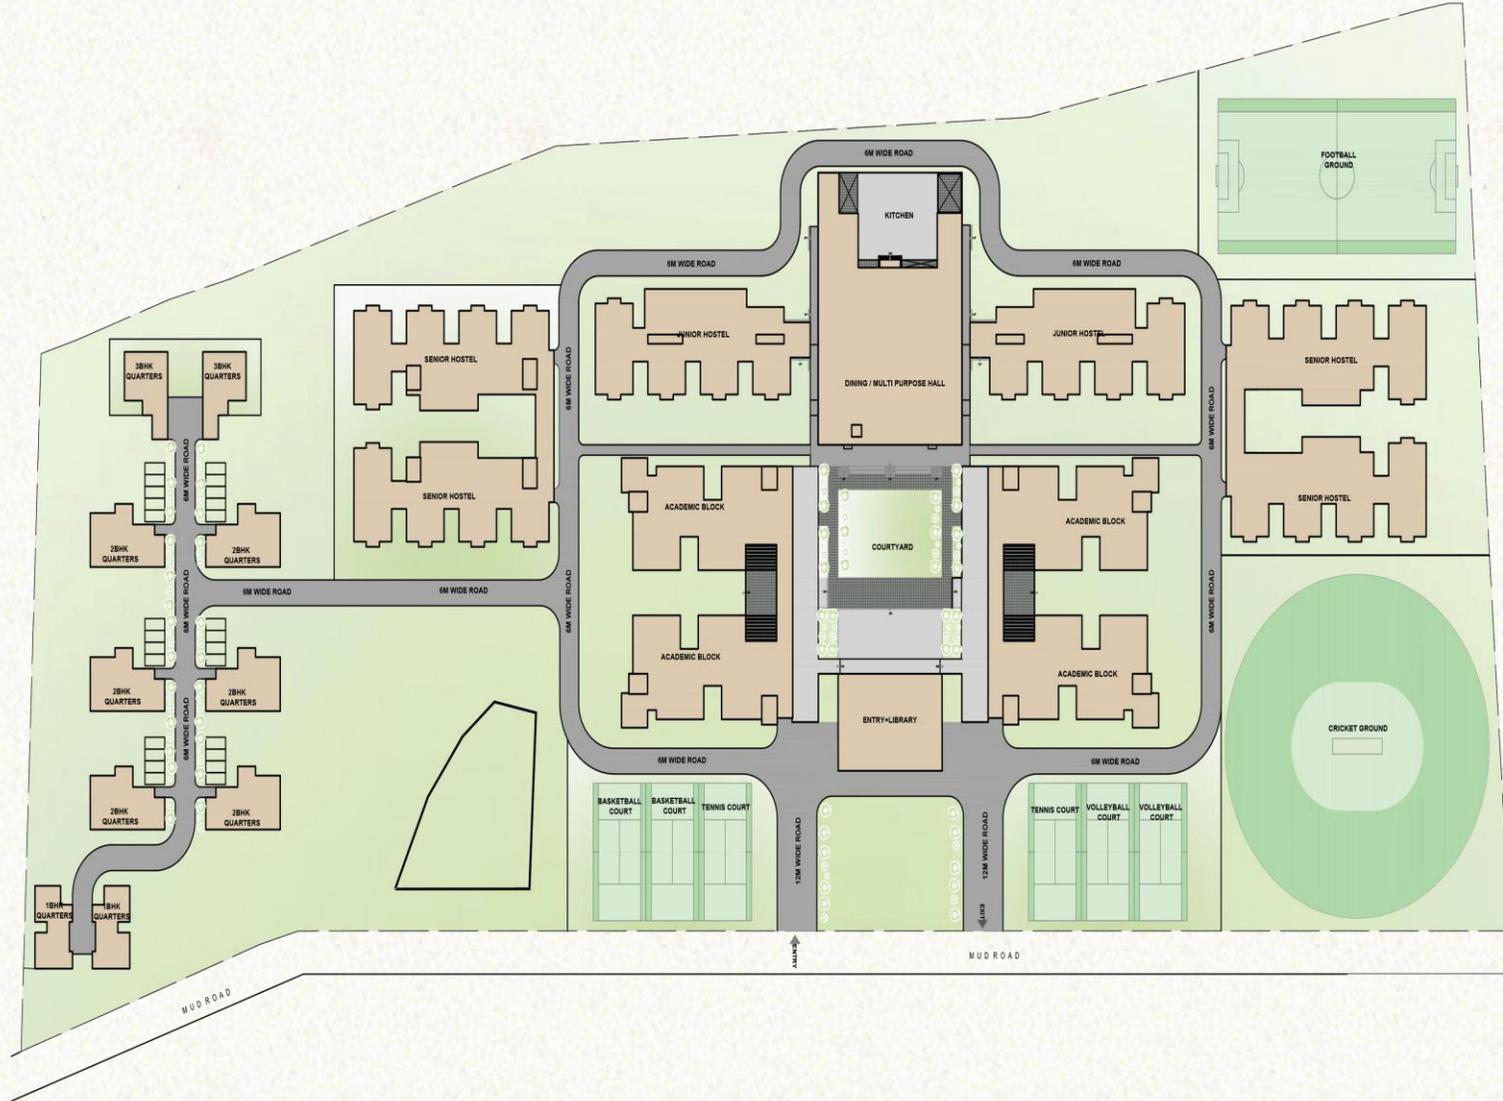

# YIIRS- RAJENDRANAGAR

<b>Village</b>	Rajendranagar
<b>Mandal</b>	Rajendranagar
<b>District</b>	Rangareddy
<b>Survey No</b>	Sy.No. 328, 331 & 332
<b>Land Extent</b>	Ac 20
<b>Contractor</b>	
<b>Consultant</b>	M/s Usha Reddy Consultants
<b>Site Issues</b>	Site is taken-over by TSIIIC. New site is requested.

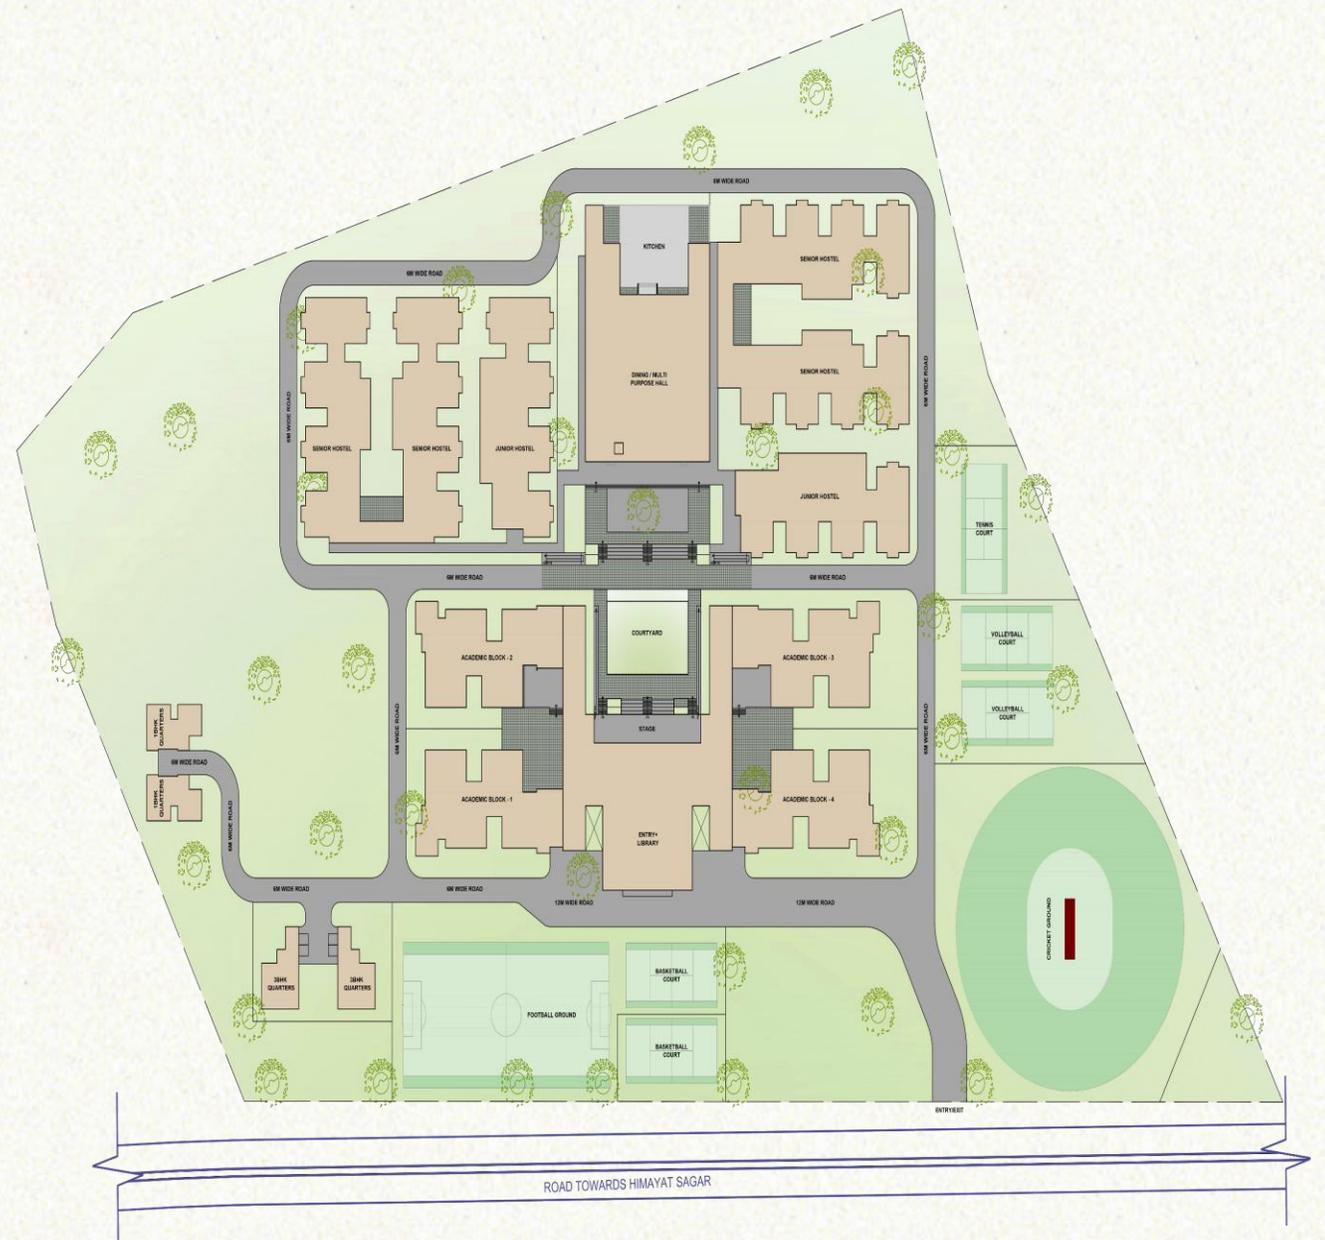

# YIIRS- TANDUR

<b>Village</b>	Yalal
<b>Mandal</b>	Yalal
<b>District</b>	Vikarabad
<b>Survey No</b>	Sy.No.
<b>Land Extent</b>	Ac 23
<b>Contractor</b>	
<b>Consultant</b>	M/s. Usha Reddy Consultants
<b>Site Issues</b>	Proposal is with the CCLA.



# YIIRS- PARGI

**Village** Tunukulagadda Parigi  
**Mandal** Parigi  
**District** Vikarabad  
**Survey No** Sy.No. 530  
**Land Extent** Ac 20.00  
**Contractor**  
**Consultant** M/s Usha Reddy Consultants



YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOL  
GOVERNMENT OF TELANGANA

UR ARCHITECTS



# YIIRS KALWAKURTHY

<b>Village</b>	Khanapur
<b>Mandal</b>	Talakondapally
<b>District</b>	Nagarkurnool
<b>Survey No</b>	Sy.No.499
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	M/s. BSR Infratech India Ltd
<b>Consultant</b>	M/s. Usha Reddy Associates
<b>Site Issues</b>	Proposal is with the CCLA.



# YIIRS- JADCHERLA

Village	Peddaipally
Mandal	Balanagar
District	Mahabubnagar
Survey No	Sy.No.224
Land Extent	Ac 18.02
Contractor	M/s. Megha Engineering and Infrastructure Ltd
Consultant	M/s. Continental Designs



# YIIRS- MAKTAL

**Village** Golapally  
**Mandal** Makthal  
**District** Narayanpet  
**Survey No** Sy.No.126  
**Land Extent** Ac 14.03  
**Contractor** M/s. Megha Engineering and Infrastructure Ltd  
**Consultant** M/s. Continental Design



# YIIRS- DEVARAKADRA

<b>Village</b>	Damgnapur
<b>Mandal</b>	Chinnachinthakunta
<b>District</b>	Mahabubnagar
<b>Survey No</b>	Sy.No. 263
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	M/s. Megha Engineering and Infrastructure Ltd
<b>Consultant</b>	M/s. Continental Design



# YIIRS- NARAYANPET

<b>Village</b>	Lingampally
<b>Mandal</b>	Narayanpet
<b>District</b>	Narayanpet
<b>Survey No</b>	Sy.No.30
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	M/s Megha Engineering and Infrastructure Ltd
<b>Consultant</b>	M/s. Continental Designs



# YIIRS- MAHABUBNAGAR

<b>Village</b>	Mahbubnagar
<b>Mandal</b>	Mahbubnagar
<b>District</b>	Mahbubnagar
<b>Survey No</b>	812/1
<b>Land Extent</b>	Ac 25.00
<b>Contractor</b>	M/s. Megha Engineering and Infrastructure Ltd
<b>Consultant</b>	M/s. Continental Designs
<b>Site Issues</b>	Allotted site is not feasible. Alternate site is requested.

# YIIRS NAGARKURNOOL

<b>Village</b>	Thudukurthy
<b>Mandal</b>	Nagarkurnool
<b>District</b>	Nagarkurnool
<b>Survey No</b>	Sy.No.816
<b>Land Extent</b>	Ac 20.00
<b>Contractor</b>	M/s BSR Infratech India Ltd
<b>Consultant</b>	M/s. Aarvee Associates



# YIIRS-ACCHAMPET

**Village** Raiched  
**Mandal** Uppununthala  
**District** Nagarkurnool  
**Survey No** Sy.No.61  
**Land Extent** Ac 20.00  
**Contractor** M/s. BSR Infratech India Ltd  
**Consultant** M/s. Aarvee Associates

## LEGEND

1. SECURITY & PARENTS WAITING HALL
2. ACADEMIC BLOCK
3. DINING BLOCK
4. DORMITORY BLOCK JUNIORS
5. DORMITORY BLOCK SENIORS
6. STAFF QUARTERS
7. PLAY FIELDS
8. PLAYGROUND
9. ELECTRICAL YARD
10. STP
11. SECURITY CABIN
12. SUMP



# YIIRS-WANAPARTHY

Village	Wanaparth
Mandal	Wanaparth
District	Wanaparth
Survey No	Sy.No.55/2
Land Extent	Ac 25.00
Contractor	M/s BSR Infratech India Ltd
Consultant	M/s . Aarvee Associates



- LEGEND**
- 1. SECURITY & PARENTS WAITING HALL
  - 2. ACADEMIC BLOCK
  - 3. DINING BLOCK
  - 4. DORMITORY BLOCK SENIORS
  - 5. DORMITORY BLOCK JUNIORS
  - 6. STAFF QUARTERS
  - 7. PLAY FIELDS
  - 8. PLAYGROUND
  - 9. ELECTRICAL YARD
  - 10. STP
  - 11. SECURITY CABIN
  - 12. SUMP

# YIIRS GADWAL

<b>Village</b>	K.T Doddi
<b>Mandal</b>	K.T Doddi
<b>District</b>	Jogulamba Gadwal
<b>Survey No</b>	Sy.No.99
<b>Land Extent</b>	Ac 25.00
<b>Contractor</b>	M/s. BSR Infratech India Ltd
<b>Consultant</b>	M/s. Aarvee Associates



# ENVIRONMENTAL CLEARANCES FOR THE TELANGANA YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS

<b>FIRST PHASE</b>				
<b>Sl. No.</b>	<b>Assembly Constituency</b>	<b>Irrigation Clearances</b>	<b>Forest Clearances</b>	<b>Required data/Remarks</b>
		<b>Applicability</b>	<b>Applicability</b>	
1	Kodangal	Yes	No	Site is changed
2	Husnabad	No	Yes	Required forest NoC
3	Manthani	Yes	Yes	Required Irrigation & Forest NoC
4	Mulugu	No	Yes	Required Forest Noc & land allotment copy
5	Kollapur	Yes	No	Required Irrigation NoC & land allotment copy
6	Palair	Yes	No	Required Irrigation NoC
7	Warangal East	Yes	No	Irrigation NoC
8	Huzurnagar	Yes	No	Site plan as per Irrigation Noc
9	Nalgonda	No	No	Environmental Clearance certificate is obtained.
10	Madhira	Yes	No	Required for the remaining land area document.
11	Shadnagar	No	No	Required land allotment order.
12	Andole	No	No	Report preparation completed & land allotment copy pending .
13	Vikarabad	No	No	Report preparation completed & land allotment copy pending .
14	Khammam	No	No	Correction in site plan (High tension power line issue)-pending

# ENVIRONMENTAL CLEARANCES FOR THE TELANGANA YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS

S.NO	ASSEMBLY CONSTITUENCY	SITE VISIT STATUS
<b>ERSTWHILE ADILABAD DISTRICT</b>		
15	Asifabad	Completed
16	Bellampalli	Completed
17	Mancherial	Completed
18	Khanapur	Completed
19	Chennur	Completed
<b>ERSTWHILE KARIMNAGAR DISTRICT</b>		
20	Peddapalli	Completed
21	Ramagundem	Completed
22	Dharmapuri	Completed
23	Choppadandi	Completed
24	Manakondur	Completed

# ENVIRONMENTAL CLEARANCES FOR THE TELANGANA YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS

S.NO	ASSEMBLY CONSTITUENCY	SITE VISIT STATUS
<b>ERSTWHILE KHAMMAM</b>		
25	Aswaraopet	Completed
26	Bhadrachalam	Completed
27	Kothgudem	Completed
28	Pinapaka	Completed
29	Sathupalle	Completed
30	Wyra	Completed
31	Yellendu	Completed
<b>ERSTWHILE MAHABUBNAGAR DISTRICT</b>		
32	YIIRS Kodangal	Completed
33	Jadcherla	Completed
34	Devarkadra	Completed
35	Narayanet	Completed
36	Makathal	Completed
37	Nagarkurnool	Completed
38	Achampet (SC)	Completed
39	Wanaparhty	Completed
40	Gadwal	Completed

# ENVIRONMENTAL CLEARANCES FOR THE TELANGANA YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS



S.NO	ASSEMBLY CONSTITUENCY	SITE VISIT STATUS
<b>ERSTWHILE WARNAGAL</b>		
41	Ghanpur (Station)	Completed
42	Palakurthi	Completed
43	Dornkal	Completed
44	Mahabubabad	Completed
<b>ERSTWHILE RANGAREDDY</b>		
45	Medchal	Completed

# YOUNG INDIA INTEGRATED RESIDENTIAL SCHOOLS Proposed in the State of Telangana



## Projects in Parliament Constituencies

ADILABAD (ST)	7
BHUVANAGIRI	7
CHEVELLA	8
HYDERABAD	1
KARIMNAGAR	7
KHAMMAM	7
MAHABUBABAD (ST)	7
MAHABUBNAGAR	7
MALKAJGIRI	7
MEDAK	5
NAGARKURNOOL (SC)	7
NALGONDA	7
NIZAMABAD	7
PEDDAPALLE (SC)	7
SECUNDERABAD	7
WARANGAL_WEST_(SC)	7
ZAHIRABAD	7
<b>Total Proposed</b>	<b>105</b>

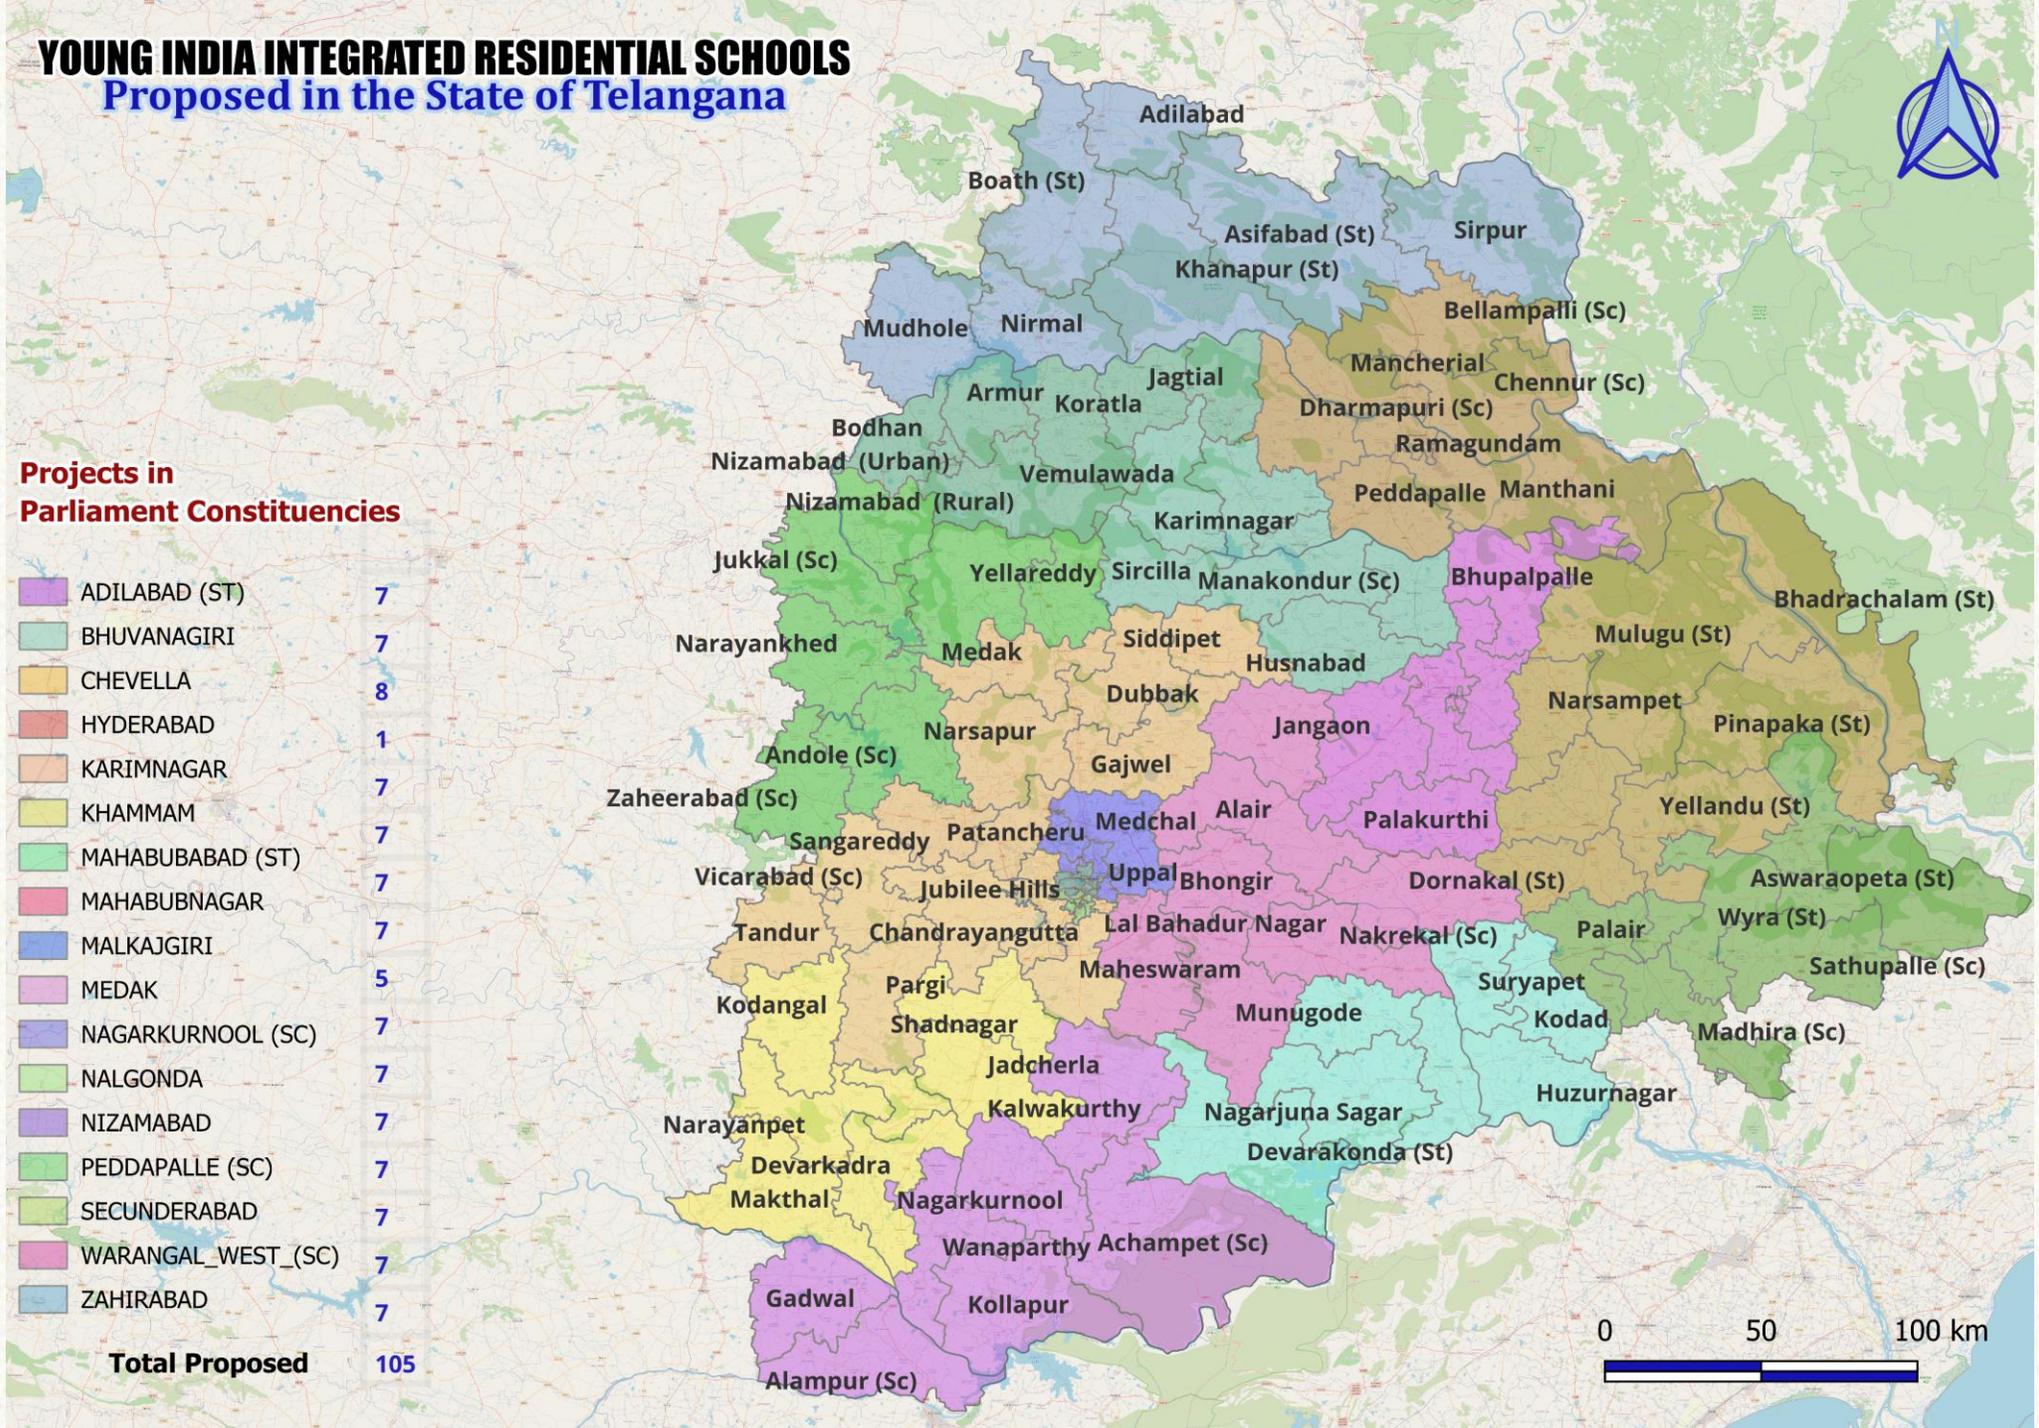



Thank You Sir
